



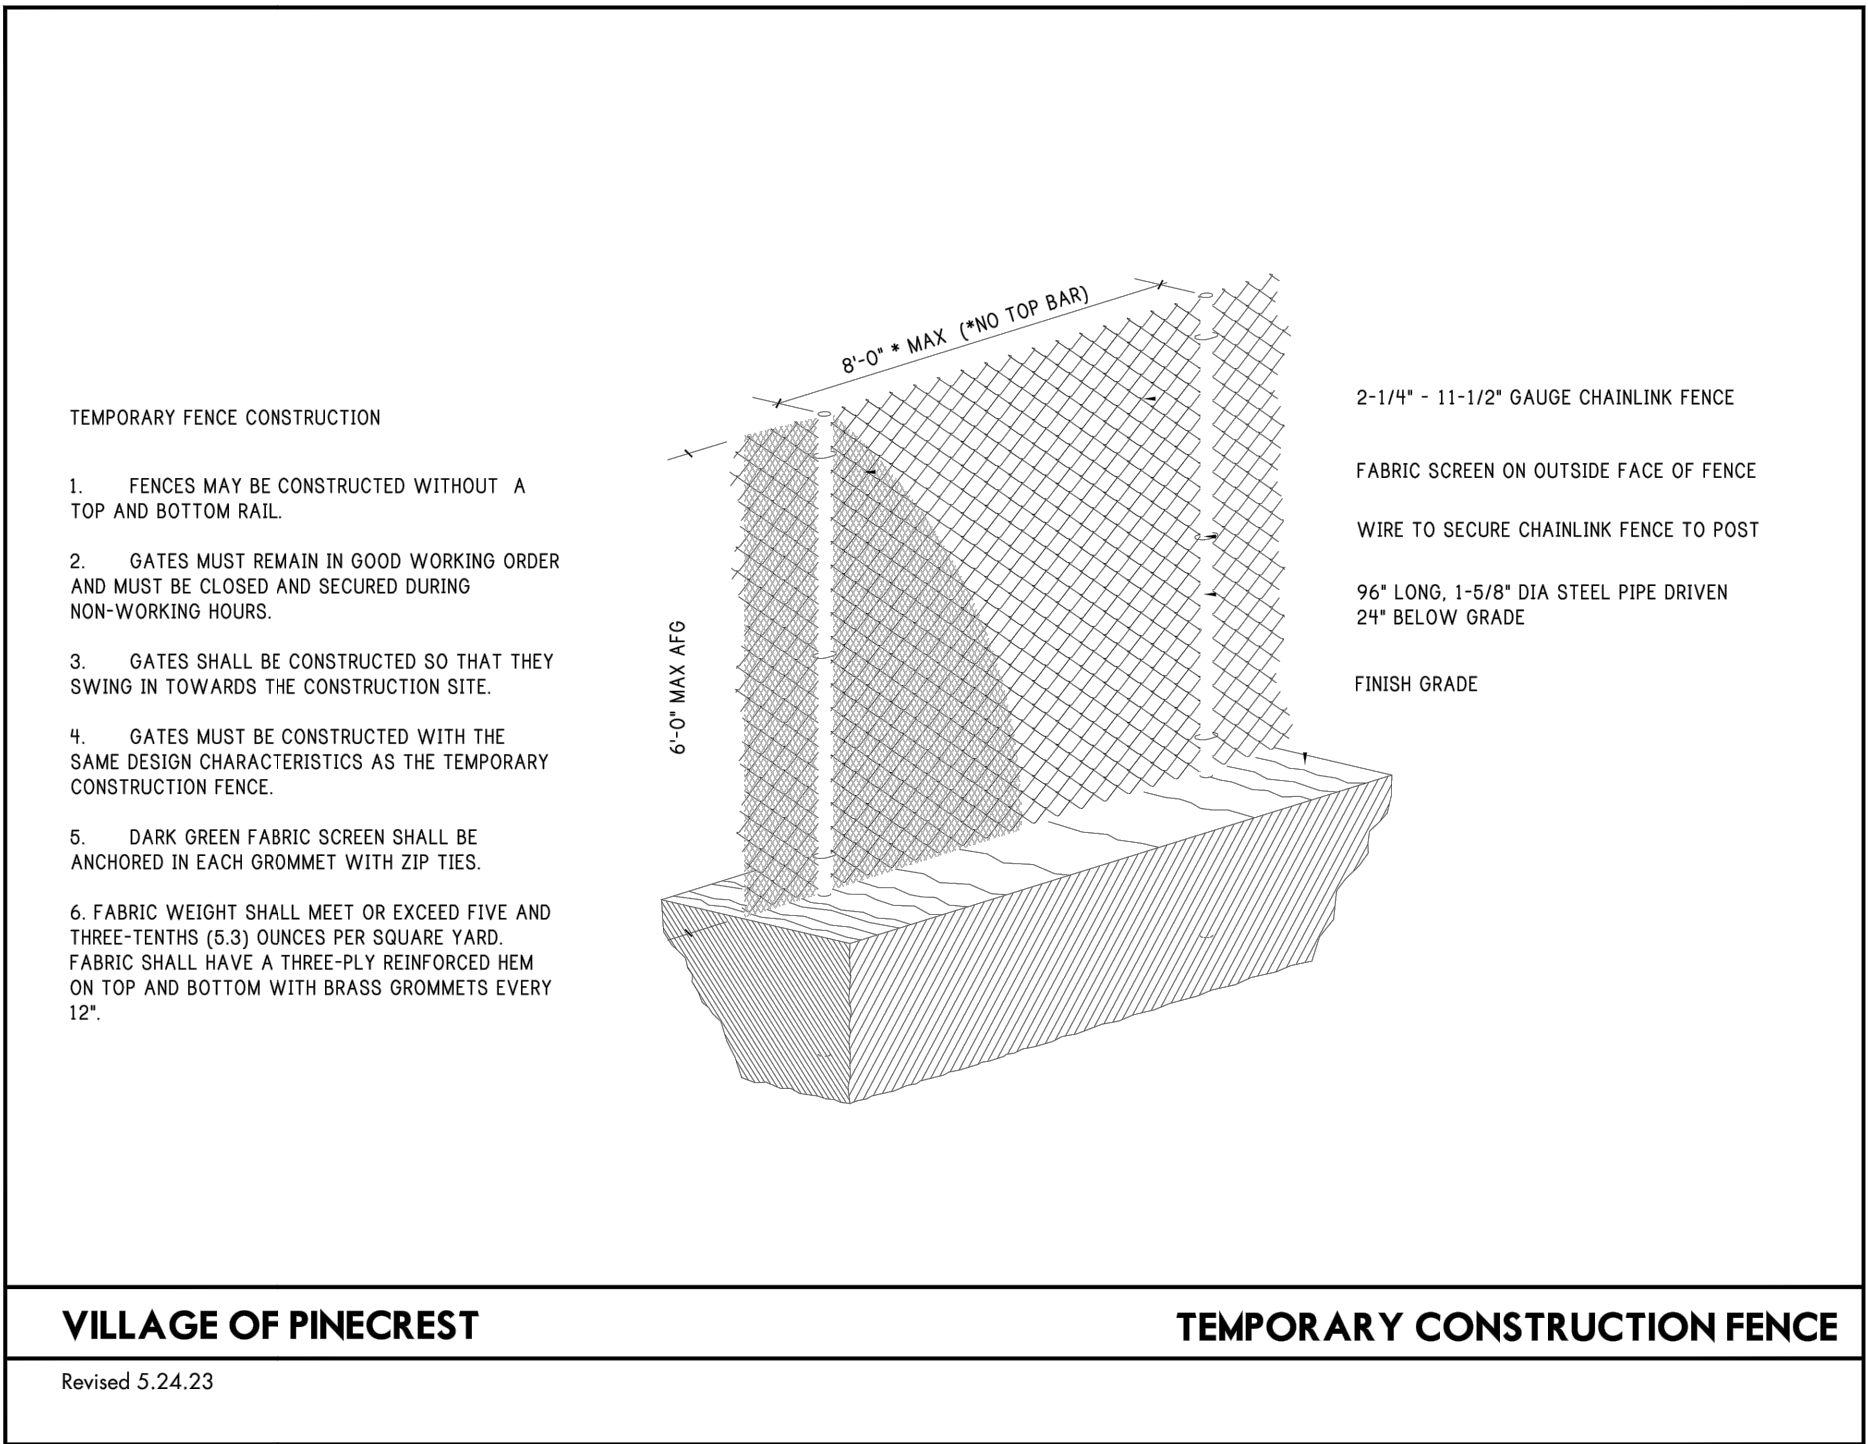

1 TEMPORARY CONSTRUCTION FENCE

N.T.S.

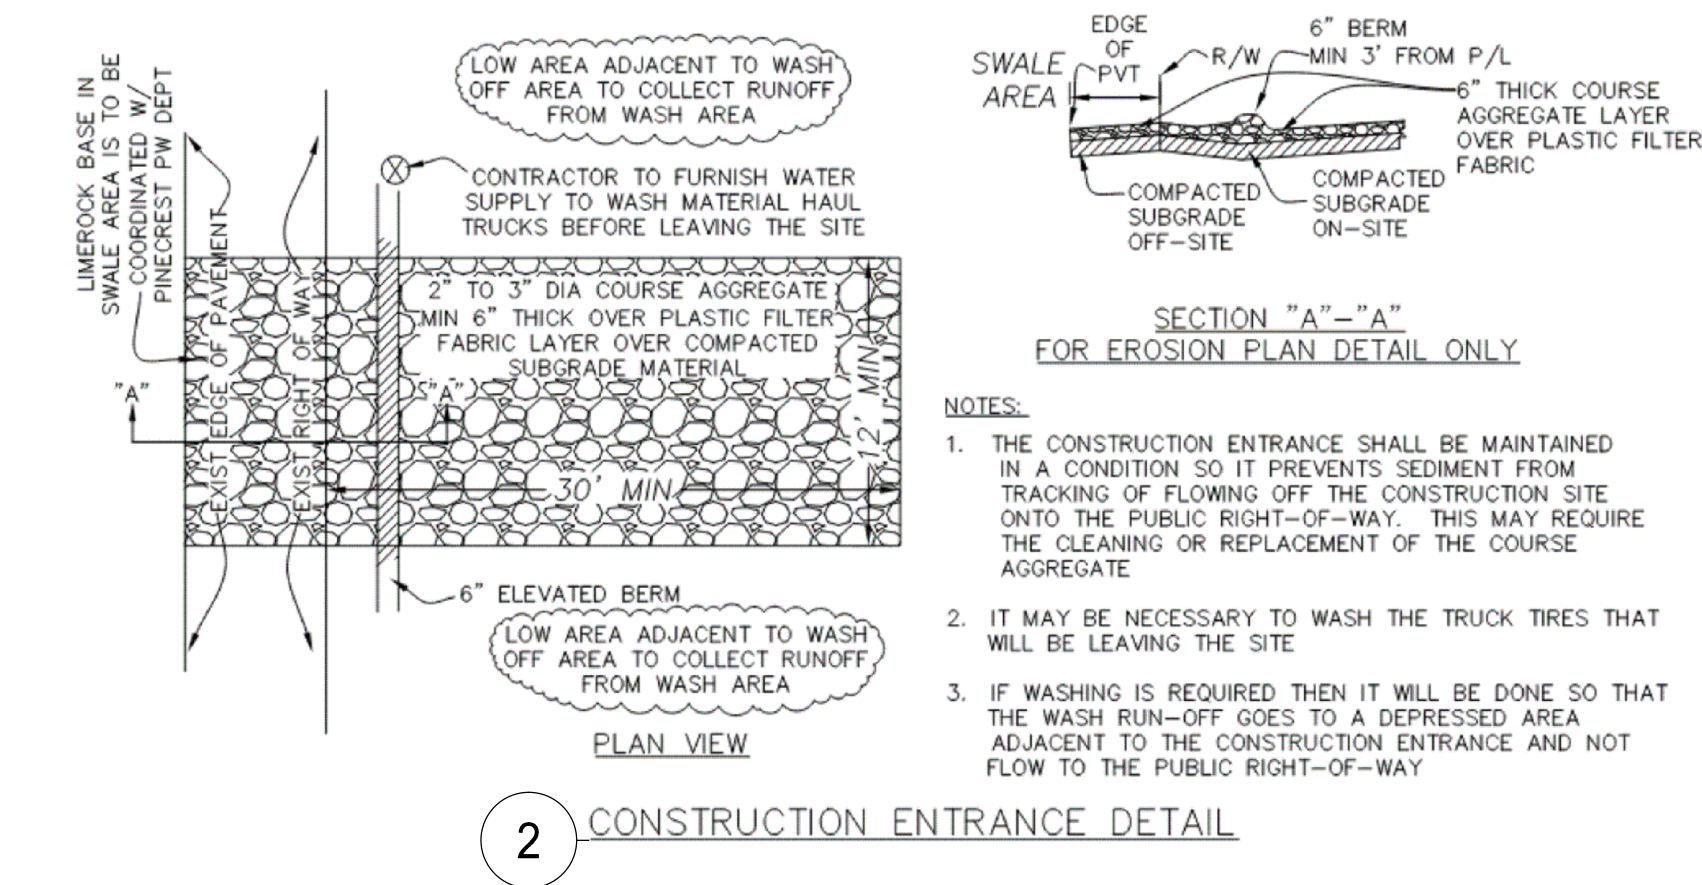


EROSION CONTROL GENERAL NOTES:

1. TREE PROTECTION AND PRUNING SHALL BE ACCOMPLISHED AS DETAILED IN SPECIAL PROVISIONS, THE CONSTRUCTION PLANS AND OR THE VILLAGE OF PINECREST'S PUBLIC WORKS STANDARDS AND/OR MIAMI DADE COUNTY'S TREE SECTION STANDARDS
2. ALL EROSION CONTROL FEATURES AS PROVIDED IN THE SWPPP ARE TO BE INSTALLED AT ALL AREAS OF EXCAVATION OR FILL FOR WATER, SEWER AND DRAINAGE FACILITIES. ALL EXIST AND PROPOSED DRAINAGE CATCH BASINS SHALL BE PROTECTED PER THE DETAILS SHOWN
3. ALL EROSION CONTROL FEATURES ARE TO BE MAINTAINED FOR THE DURATION OF THE PROJECT IN ACCORDANCE WITH THE MIAMI DADE COUNTY'S RER-DEEM NPDES REQUIREMENTS
4. ALL EROSION MATERIAL AND EXCAVATED MATERIAL SHALL BE STORED ON SITE WHERE POSSIBLE. IF THESE MATERIALS CAN NOT BE STORED ON SITE THEN THEY SHALL BE TRANSPORTED TO AN APPROVED MATERIAL DISPOSAL SITE
5. ANY INEFFECTIVE OR DAMAGED SYNTHETIC BALES OR "SOCKS" SHALL BE REPAIRED OR REPLACED AS REQUIRED
6. ALL EXISTING AND/OR PROPOSED STORMWATER INLETS (AREA BASINS, DITCH, C&G, P6, ETC.) SHALL BE PROTECTED FROM SEDIMENT FLOWING INTO THE INLET STRUCTURE WITH SYNTHETIC BALES OR "SOCKS" UNTIL THE PROJECT HAS BEEN COMPLETED
7. STOCKPILED MATERIALS SHALL BE STORED IN A FASHION TO PREVENT THE STORED MATERIALS FROM FLOWING OFF-SITE TO A PUBLIC RIGHT-OF-WAY OR TO ANY EXISTING OR PROPOSED STORMWATER INLET
8. THE EROSION CONTROL PLAN FEATURES SHALL BE INSPECTED ON A DAILY BASIS. A DAILY INSPECTION LOG SHALL BE KEPT ON SITE ALL ALL CORRECTIONS TO THE FEATURES SHALL BE NOTED IN THE LOG


SWPPP NARRATIVE:

1. THE SITE AREA WITHIN THE PROPERTY LINES IS ROUGHLY 0.402± ACRES
2. THE PROPOSED WORK ON THIS PROJECT WILL CONSIST OF THE EXCAVATION FOR THE PROPOSED HOUSE FOUNDATION AND FOR SITE GRADING
3. THE CONTRACTOR WILL MAINTAIN PROTECTION OF ALL EXISTING DRAINAGE INLETS FROM THE INTRODUCTION OF ANY LOOSE SEDIMENTS FROM THE PROPOSED WORK ACTIVITIES
4. THE USE OF VARIOUS PROTECTIVE DEVICES (I.E. SAND BAGS, FILTER FABRIC, SYNTHETIC BALES AND SOCKS, SEDIMENT SCREEN FENCES, WIN SCREENS ETC.) WILL BE USED TO COMPLY WITH THE NPDES REQUIREMENTS FOR A SWPPP
5. ALL EXCAVATED MATERIAL WILL EITHER STORED ON-SITE TO BE USED ON OTHER PORTIONS OF THE PROJECT OR DISPOSED OF OFF-SITE AT AN APPROVED WASTE DISPOSAL FACILITY
6. ALL MATERIAL STORED ON-SITE WILL BE COVERED IF APPLICABLE TO PREVENT ANY LOOSE MATERIAL FROM LEAVING THE SITE
7. DUMPSTER WILL BE PROVIDED AS NEED TO STORE WASTE MATERIAL GENERATED FROM THE HOUSE CONSTRUCTION
8. TRUCKS HAULING FILL OR DISPOSAL MATERIALS TO AND FROM THE SITE WILL BE COVERED WITH A TARP TO PREVENT LOOSE MATERIAL FROM LEAVING THE TRUCK
9. A TRUCK WASH DOWN AREA WILL BE PROVIDED AS NECESSARY TO REDUCE THE PROBABILITY OF MATERIAL LEAVING THE SITE
10. NO CONTAMINATED STORMWATER DISCHARGES ARE ANTICIPATED FOR THIS SITE AS THIS SITE IS NOT LISTED AS A CONTAMINATED SITE WITH RER
11. THE SWPPP WILL BE MAINTAINED THRU THE COMPLETION OF THE PROJECT.
12. ALL SWPPP PROTECTION DEVICES SHALL BE REPAIRED OR REPLACED AS REQUIRED AS TO MAINTAIN THE SWPPP IN PROPER WORK ORDER
13. A MAINTENANCE LOG OF DAILY MAINTENANCE INSPECTIONS SHALL BE KEPT AVAILABLE AT THE SITE BY THE GENERAL CONTRACTOR IN CONTROL OF THE PROJECT

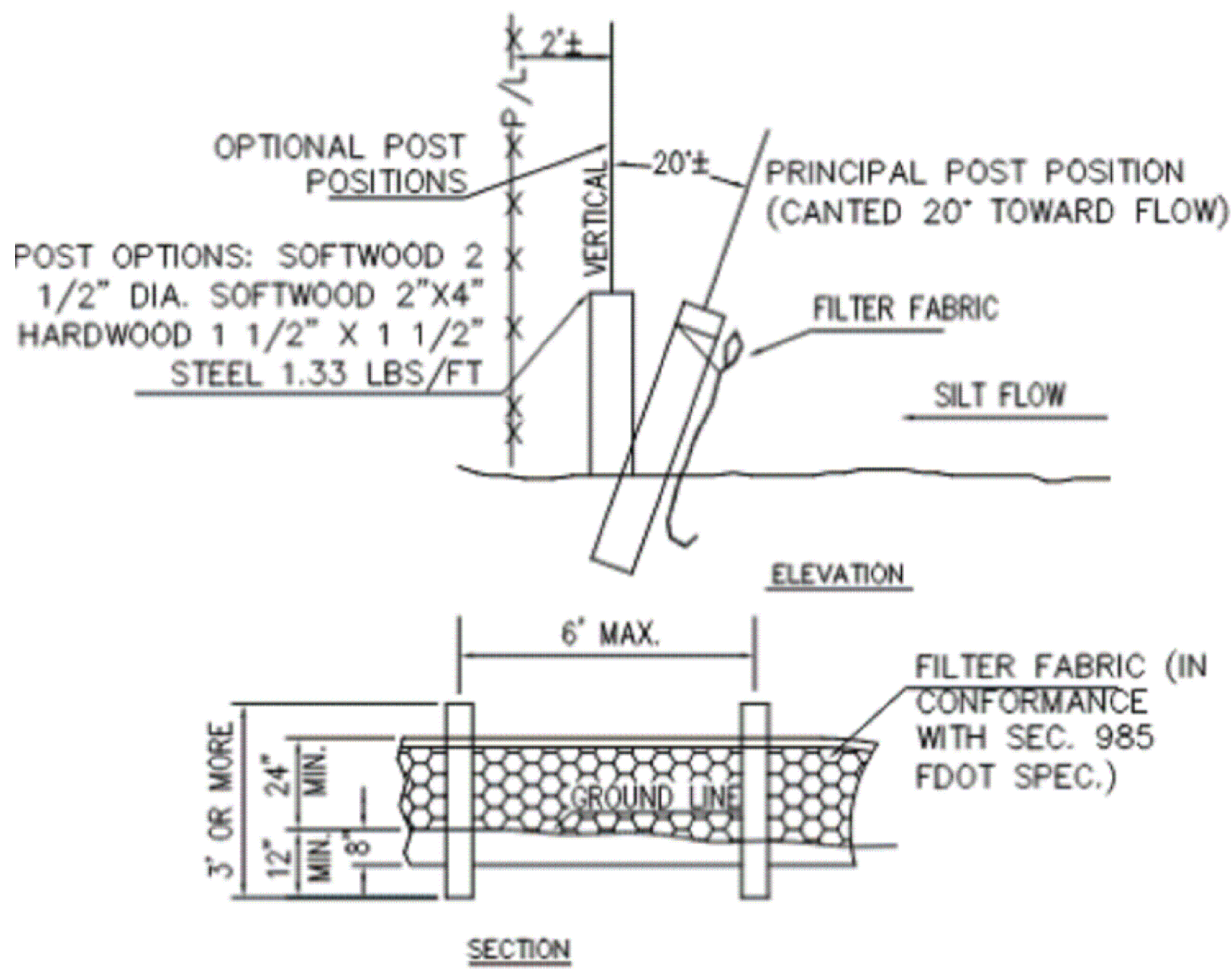

3 TEMPORARY SILT FENCE

1. SILT FENCES (EROSION CONTROL FENCE (---)) SHALL BE PROVIDED AS SHOWN ALONG THE PROPERTY LINE TO PREVENT CONSTRUCTION DEBRIS FROM LEAVING THE CONSTRUCTION SITE
 2. THE SITE FENCE SHALL BE PLACED A MINIMUM OF TWO FEET INSIDE THE PROPERTY LINE TO ALLOW THE INSTALLATION OF A PERIMETER WIND SCREEN & CONSTRUCTION FENCE
 3. A PERIMETER SIX FOOT HIGH CHAIN LINK FENCE COVERED WITH A WIND SCREEN SHALL BE INSTALLED ALONG THE PROPERTY LINE
- EROSION CONTROL --- FENCE SYMBOL

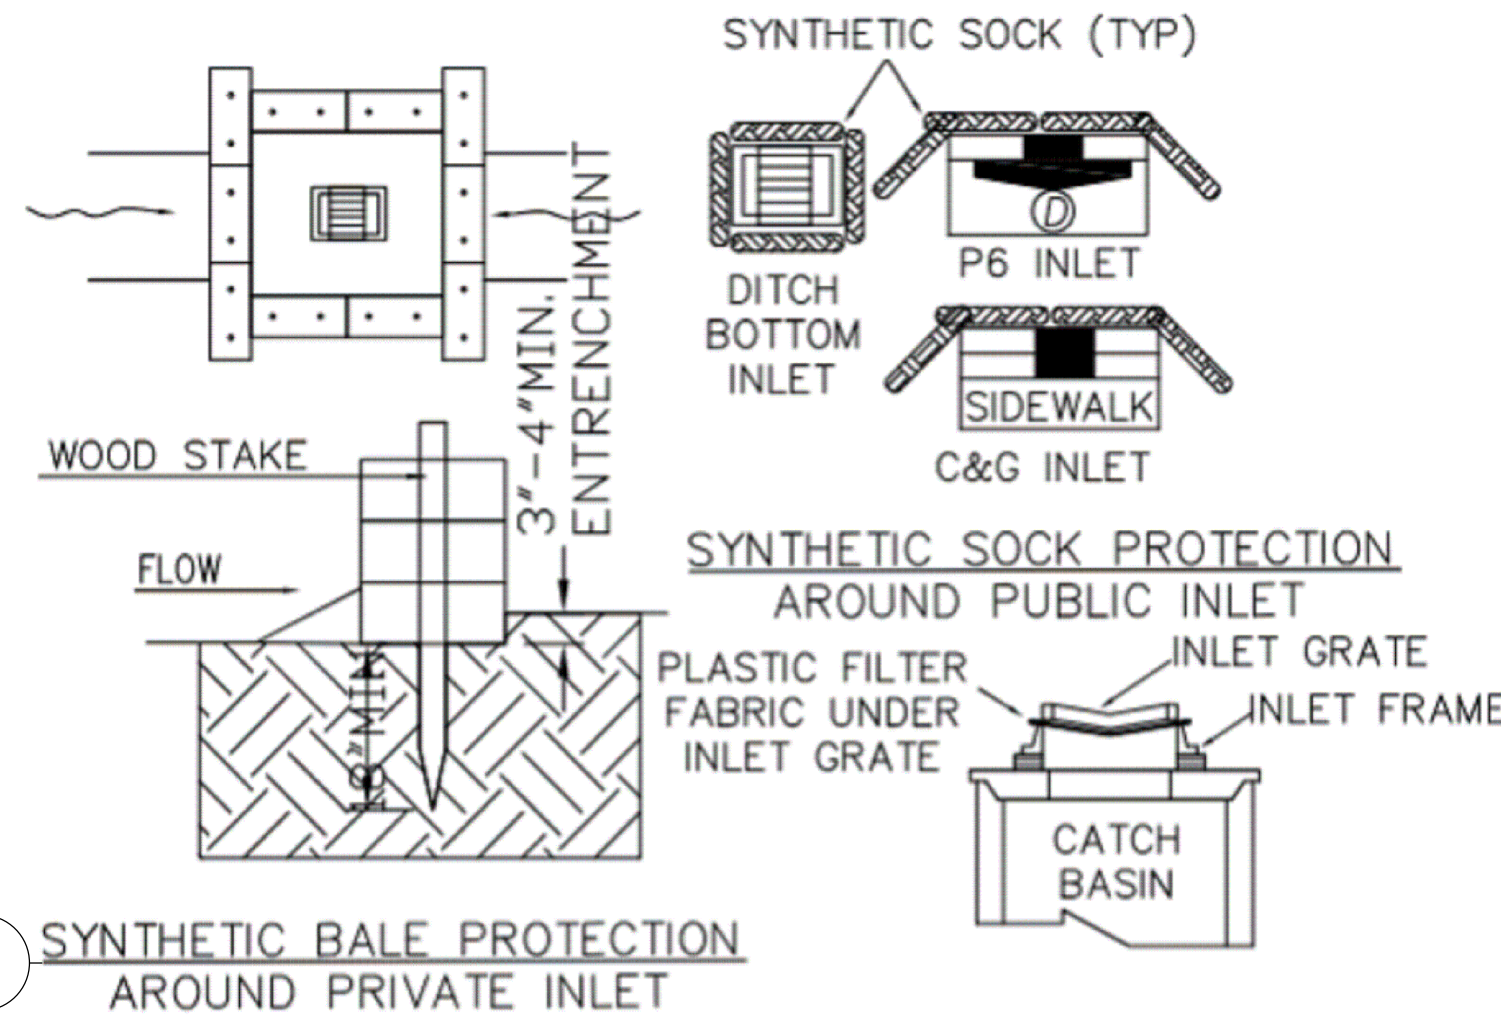

4 SYNTHETIC BALE PROTECTION AROUND PRIVATE INLET

- NOTES:
1. SYNTHETIC BALES SHALL BE TRENCHED 3" TO 4" AND ANCHORED WITH 2 - 1" X 2" (OR 1" DIAM.) X 4" WOOD STAKES. STAKES OF OTHER MATERIAL OR SHAPE PROVIDING EQUIVALENT STRENGTH MAY BE USED IF APPROVED BY THE ENGINEER
 2. ADJACENT SYNTHETIC BALES SHALL BE BUTTED FIRMLY TOGETHER. UNAVOIDABLE GAPS SHALL BE PLUGGED WITH HAY OR STRAW TO PREVENT SILT FROM PASSING
 3. SYNTHETIC BALES SHALL BE INSTALLED AT ALL NEW INLETS ON PRIVATE PROPERTY AND SYNTHETIC "SOCKS" ON EXISTING INLETS IN THE PUBLIC RIGHT O WAY DURING CONSTRUCTION
 4. CONTRACTOR TO INSTALL PLASTIC FILTER FABRIC UNDER INLET GRATE ON ALL NEW INLETS AND IT SHALL REMAIN THERE FOR THE DURATION OF THE CONSTRUCTION

RAMOSMARTINEZarchitects

MIAMI
655 W FLAGLER ST.
SUITE 205
MIAMI, FL 33130

REGISTRATION: A.A. 26000528
WEBSITE: www.rmqa.com
TELEPHONE: 305-548-3006

NEW YORK
11 ERIE STREET
2ND FLOOR
JERSEY CITY, NJ 07302

NEW RESIDENCE
FOR
ELIGES INVESTORS CONSTRUCTION
AT
9841 SW 73rd COURT
PINECREST, FLORIDA 33156

STRUCTURAL ENGINEER: _____ SEAL: _____
EASTERN ENGINEERING
3401 NW 80th AVE. SUITE 370
MIAMI, FLORIDA 33122 305-599-8133

MECHANICAL ENGINEER: _____
ORLANDO RANGEL, P.E. - 60225
9940 SW 37th STREET, MIAMI, FLORIDA 33165
TEL: 786-547-3517


CIVIL ENGINEER: _____
ANDRE D. MARTINEZ, P.E. - 85425
AM CIVIL ENGINEERS & PLANNERS
860 SW 21st STREET MIAMI, FLORIDA 33135
TEL: 786-289-9414 amcivildesign@gmail.com

LANDSCAPE ARCHITECT: _____

ARCHITECT:
HUMBERTO RAMOS
AIA 0077833

COPYRIGHT - 2021 - RAMOSMARTINEZarchitects, inc.
THE DESIGNS, IDEAS AND DETAIL INDICATED OR REPRESENTED BY THIS DRAWING, CREATED AND DEVELOPED FOR USE ON THIS PROJECT, ARE OWNED BY AND THE LEGAL PROPERTY OF RAMOSMARTINEZ architects, inc. USE, REPRODUCTION, DISTRIBUTION OR ALTERATION IS PROHIBITED WITHOUT WRITTEN AUTHORIZATION BY THE ARCHITECT.

KEY PLAN:



COMM. NO.: 17-117 NO: REVISION: DATE:

DATE: JANUARY, 2022 Build Dep. Comments 12/18/2024

DRAWN BY: _____

CONTENT:

TEMPORARY CONSTRUCTION
FENCE & SWPPP DETAILS

SHEET NUMBER:

A-2
