

RESIDENTIAL ENERGY CONSERVATION CODE DOCUMENTATION CHECKLIST

Florida Department of Business and Professional Regulation Simulated Performance Alternative (Performance) Method

Applications for compliance with the 2022 Florida Building Code, Energy Conservation via the Residential Simulated Performance Alternative shall include:

- ☒ This checklist
- ☒ Form R405-2022 report
- ☒ Input summary checklist that can be used for field verification (usually four pages/may be greater)
- ☒ Energy Performance Level (EPL) Display Card (one page)
- ☒ HVAC system sizing and selection based on ACCA Manual S or per exceptions provided in Section R403.7
- ☒ Mandatory Requirements (five pages)

Required prior to CO:

- ☒ Air Barrier and Insulation Inspection Component Criteria checklist (Table R402.4.1.1 - one page)
- ☒ A completed 2022 Envelope Leakage Test Report (usually one page); exception in R402.4 allows dwelling units of R-2 Occupancies and multiple attached single family dwellings to comply with Section C402.5
- ☐ If Form R405 duct leakage type indicates anything other than "default leakage", then a completed 2020 Duct Leakage Test Report - Performance Method (usually one page)

Project Name: PINECREST RESIDENCE				Builder Name:			
Street: 7725 SOUTHWEST 114 STREET				Permit Office:			
City, State, Zip: MIAMI, FL, 33156				Permit Number:			
Owner:				Jurisdiction:			
Design Location: FL, Miami				County: Miami-Dade(Florida Climate Zone 1)			

1. New construction or existing		New (From Plans)		10. Wall Types(6900.4 sqft.)		Insulation		Area	
2. Single family or multiple family		Detached		a. Concrete Block - Int Insul, Exterior		R=5.0		6547.60 ft ²	
3. Number of units, if multiple family		1		b. Frame - Steel, Adjacent		R=5.0		352.78 ft ²	
4. Number of Bedrooms		6		c. N/A					
5. Is this a worst case?		No		d. N/A					
6. Conditioned floor area above grade (ft²)		6331		11. Ceiling Types(6331.0 sqft.)		Insulation		Area	
Conditioned floor area below grade (ft²)		0		a. Flat ceiling under att (Vented)		R=30.0		3631.00 ft ²	
7. Windows(1935.8 sqft.) Description		Area		b. Sloped ceiling under a (Vented)		R=30.0		2700.00 ft ²	
a. U-Factor:	Sgl, U=1.05	1935.80 ft ²		c. N/A					
SHGC:	SHGC=0.31			12. Roof(Flat tile/slate, Vented) Deck R=0.0				6673 ft ²	
b. U-Factor:	N/A	ft ²		13. Ducts, location & insulation level			R	ft ²	
SHGC:				a. Sup: Attic, Ret: Attic, AH: SPACE 1			6	395	
c. U-Factor:	N/A	ft ²		b. Sup: Attic, Ret: SPACE 2, AH: SPACE 2			6	305	
SHGC:				c. 1 additional duct system(s)			(see details)		
Area Weighted Average Overhang Depth:		4.633 ft		14. Cooling Systems		kBtu/hr		Efficiency	
Area Weighted Average SHGC:		0.310		a. Central Unit		55.5	SEER2:15.20		
8. Skylights		Description	Area	b. Central Unit		55.5	SEER2:15.20		
U-Factor:(AVG)	N/A	N/A ft ²		c. Central Unit		34.2	SEER2:15.20		
SHGC(AVG):	N/A			15. Heating Systems		kBtu/hr		Efficiency	
9. Floor Types		Insulation	Area	a. Electric Strip Heat		34.1	COP:1.00		
a. Slab-On-Grade Edge Insulation	R= 0.0	6331.00 ft ²		b. Electric Strip Heat		34.1	COP:1.00		
b. N/A	R=	ft ²		c. Electric Strip Heat		23.9	COP:1.00		
c. N/A	R=	ft ²		16. Hot Water Systems					
				a. PropaneTankless			Cap: 1 gallons		
				b. Conservation features			EF: 0.590		
				17. Credits				None	Pstat

PASS

DATE: _____

- Page 1

INPUT SUMMARY CHECKLIST REPORT

PROJECT												
Title:	PINECREST RESIDENCE				Address type:		Street Address					
Building Type:	User				Bedrooms:	6		Lot #:	---			
Owner:					Conditioned Area:	6331		Block/SubDivision:	---			
					Total Stories:	1		PlatBook:	---			
Builder Name:					Worst Case:	No		Street:	7725 SOUTHWEST 114 STREET			
Permit Office:					Rotate Angle:	0		County:	Miami-Dade			
Jurisdiction:					Cross Ventilation:			City, State, Zip:	MIAMI, FL, 33156			
Family Type:	Detached				Whole House Fan:							
New/Existing:	New (From Plans)				Terrain:	Suburban						
Year Construct:					Shielding:	Suburban						
Comment:												
CLIMATE												
✓ Design Location	Tmy Site		Design Temp		Int Design Temp		Heating	Design	Daily temp			
			97.5%	2.5%	Winter	Summer	Degree Days	Moisture	Range			
___ FL, Miami	FL_MIAMI_INTL_AP		51	90	70	75	149.5	56	Low			
BLOCKS												
✓ Number	Name	Area	Volume									
___ 1	Block1	2191	23444 cu ft									
___ 2	Block2	2700	43200 cu ft									
___ 3	Block3	1440	17280 cu ft									
SPACES												
✓ Number	Name	Area	Volume	Kitchen	Occupants	Bedrooms	Finished	Cooled	Heated			
___ 1	SPACE 1	2191	23444	No	5	4	Yes	Yes	Yes			
___ 2	SPACE 2	2700	43200	Yes	0	0	Yes	Yes	Yes			
___ 3	SPACE 3	1440	17280	No	3	2	Yes	Yes	Yes			
FLOORS (Total Exposed Area = 6331 sq.ft.)												
✓ #	Floor Type	Space	Exposed Perim	Perimeter R-Value	Area	U-Factor	Joist R-Value	Tile	Wood	Carpet		
___ 1	Slab-On-Grade Edge Ins	SPACE 1	252	0	2191 ft	0.710	---	1.00	0.00	0.00		
___ 2	Slab-On-Grade Edge Ins	SPACE 2	262	0	2700 ft	0.710	---	1.00	0.00	0.00		
___ 3	Slab-On-Grade Edge Ins	SPACE 3	193	0	1440 ft	0.710	---	1.00	0.00	0.00		
ROOF												
✓ #	Type	Materials	Roof Area	Gable Area	Roof Color	Rad Barr	Solar Absor.	SA Tested	Emitt	Emitt Tested	Deck Insul.	Pitch (deg)
___ 1	Hip	Flat tile/slate	6673 ft²	0 ft²	Light	N	0.96	No	0.9	No	0	18.43
ATTIC												
✓ #	Type	Ventilation	Vent Ratio (1 in)		Area	RBS	IRCC					
___ 1	Partial cathedral ceiling	Vented	150		6331 ft²	N	N					

INPUT SUMMARY CHECKLIST REPORT

CEILING													(Total Exposed Area = 6331 sq.ft.)			
✓ #	Ceiling Type	Space	R-Value	Ins. Type	Area	U-Factor	Framing Frac.	Truss Type								
___ 1	Flat ceiling under attic(Vented)	SPACE 1	30.0	Blown	2191.0ft²	0.031	0.11	Metal								
___ 2	Sloped ceiling under attic(Vented)	SPACE 2	30.0	Blown	2700.0ft²	0.030	0.11	Wood								
___ 3	Flat ceiling under attic(Vented)	SPACE 3	30.0	Blown	1440.0ft²	0.031	0.11	Metal								

WALLS													(Total Exposed Area = 6900 sq.ft.)			
✓ #	Ornt	Adjacent To	Wall Type	Space	Cavity R-Value	Width Ft	In	Height Ft	In	Area sq.ft.	U-Factor	Sheath R-Value	Frm. Frac.	Solar Absor.	Below Grade	
___ 1	W	Exterior	Conc. Blk - Int Ins	SPACE 1	5.0	97.0	11	10.0	7	1036.3	0.132		0	0.50	0 %	
___ 2	S	Exterior	Conc. Blk - Int Ins	SPACE 1	5.0	18.0	6	10.0	7	195.8	0.132		0	0.50	0 %	
___ 3	E	Exterior	Conc. Blk - Int Ins	SPACE 1	5.0	17.0	6	10.0	7	185.2	0.132		0	0.50	0 %	
___ 4	E	Exterior	Conc. Blk - Int Ins	SPACE 1	5.0	16.0	6	10.0	7	174.6	0.132		0	0.50	0 %	
___ 5	S	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	57.0	6	12.0	0	690.0	0.132		0	0.50	0 %	
___ 6	S	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	32.0	4	7.0	4	237.1	0.132		0	0.50	0 %	
___ 7	W	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	37.0	6	7.0	4	275.0	0.132		0	0.50	0 %	
___ 8	E	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	37.0	6	7.0	4	275.0	0.132		0	0.50	0 %	
___ 9	E	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	13.0	4	12.0	0	160.0	0.132		0	0.50	0 %	
___ 10	E	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	28.0	8	12.0	0	344.0	0.132		0	0.50	0 %	
___ 11	N	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	61.0	4	10.0	10	664.4	0.132		0	0.50	0 %	
___ 12	N	Exterior	Conc. Blk - Int Ins	SPACE 2	5.0	32.0	4	7.0	4	237.1	0.132		0	0.50	0 %	
___ 13	W	Exterior	Conc. Blk - Int Ins	SPACE 3	5.0	12.0	6	12.0	0	150.0	0.132		0	0.50	0 %	
___ 14	W	Exterior	Conc. Blk - Int Ins	SPACE 3	5.0	35.0	9	12.0	0	429.0	0.132		0	0.50	0 %	
___ 15	N	Exterior	Conc. Blk - Int Ins	SPACE 3	5.0	19.0	6	12.0	0	234.0	0.132		0	0.50	0 %	
___ 16	E	Exterior	Conc. Blk - Int Ins	SPACE 3	5.0	85.0	6	12.0	0	1026.0	0.132		0	0.50	0 %	
___ 17	S	Exterior	Conc. Blk - Int Ins	SPACE 3	5.0	19.0	6	12.0	0	234.0	0.132		0	0.50	0 %	
___ 18	S	Garage	Frame - Steel	SPACE 1	5.0	33.0	4	10.0	7	352.8	0.228		0.23	0.50	0 %	

DOORS													(Total Exposed Area = 62 sq.ft.)			
✓ #	Ornt	Adjacent To	Door Type	Space	Storms	U-Value	Width Ft	In	Height Ft	In	Area					
___ 1	S	Exterior	Wood	SPACE 2	Wood	0.46	6.00	2	10.00	0	61.7ft²					

WINDOWS													(Total Exposed Area = 1936 sq.ft.)				
✓ #	Ornt	Wall ID	Frame	Panes	NFRC U-Factor	SHGC	Imp	Storm	Total Area (ft²)	Same Units	Width (ft)	Height (ft)	--Overhang-- Depth (ft)	Sep. (ft)	Interior Shade	Screen	
___ 1	S	5	Metal	Single (Clear)	Y	1.05	0.31	N	N	105.0	5	3.00	7.00	3.0	1.0	None	None
___ 2	W	1	Metal	Single (Clear)	Y	1.05	0.31	N	N	172.7	4	6.17	7.00	3.0	1.0	None	None
___ 3	W	1	Metal	Single (Clear)	Y	1.05	0.31	N	N	18.0	1	3.00	6.00	3.0	1.0	None	None
___ 4	S	2	Metal	Single (Clear)	Y	1.05	0.31	N	N	12.0	1	2.00	6.00	3.0	1.0	None	None
___ 5	S	2	Metal	Single (Clear)	Y	1.05	0.31	N	N	35.0	1	3.50	10.00	3.0	1.0	None	None
___ 6	E	4	Metal	Single (Clear)	Y	1.05	0.31	N	N	43.2	1	6.17	7.00	3.0	1.0	None	None
___ 7	S	5	Metal	Single (Clear)	Y	1.05	0.31	N	N	147.5	1	15.00	9.83	3.0	1.0	None	None
___ 8	S	5	Metal	Single (Clear)	Y	1.05	0.31	N	N	129.5	2	6.58	9.83	3.0	1.0	None	None
___ 9	S	6	Metal	Single (Clear)	Y	1.05	0.31	N	N	27.0	1	6.75	4.00	3.0	1.0	None	None
___ 10	W	7	Metal	Single (Clear)	Y	1.05	0.31	N	N	54.0	2	6.75	4.00	3.0	1.0	None	None
___ 11	E	8	Metal	Single (Clear)	Y	1.05	0.31	N	N	54.0	2	6.75	4.00	3.0	1.0	None	None
___ 12	E	9	Metal	Single (Clear)	Y	1.05	0.31	N	N	95.3	1	13.00	7.33	3.0	1.0	None	None
___ 13	E	10	Metal	Single (Clear)	Y	1.05	0.31	N	N	15.0	1	3.00	5.00	6.0	1.0	None	None
___ 14	E	10	Metal	Single (Clear)	Y	1.05	0.31	N	N	80.0	1	8.00	10.00	6.0	1.0	None	None
___ 15	N	11	Metal	Single (Clear)	Y	1.05	0.31	N	N	200.0	1	20.00	10.00	8.0	1.0	None	None
___ 16	N	11	Metal	Single (Clear)	Y	1.05	0.31	N	N	160.0	1	16.00	10.00	8.0	1.0	None	None
___ 17	W	13	Metal	Single (Clear)	Y	1.05	0.31	N	N	121.7	1	12.17	10.00	3.0	1.0	None	None

INPUT SUMMARY CHECKLIST REPORT

WINDOWS(Continued)

___ 18W	14	Metal	Single (Clear)	Y	1.05	0.31	N	N	12.0	2	3.00	2.00	6.0	1.0	None	None
___ 19W	14	Metal	Single (Clear)	Y	1.05	0.31	N	N	80.0	1	8.00	10.00	6.0	1.0	None	None
___ 20N	15	Metal	Single (Clear)	Y	1.05	0.31	N	N	160.0	1	16.00	10.00	8.0	1.0	None	None
___ 21E	16	Metal	Single (Clear)	Y	1.05	0.31	N	N	18.0	3	3.00	2.00	3.0	1.0	None	None
___ 22E	16	Metal	Single (Clear)	Y	1.05	0.31	N	N	12.0	3	2.00	2.00	3.0	1.0	None	None
___ 23E	16	Metal	Single (Clear)	Y	1.05	0.31	N	N	24.0	1	3.00	8.00	3.0	1.0	None	None
___ 24S	17	Metal	Single (Clear)	Y	1.05	0.31	N	N	160.0	1	16.00	10.00	3.0	1.0	None	None

INFILTRATION

✓ #	Scope	Method	SLA	CFM50	ELA	EqLA	ACH	ACH50	Space(s)	Infiltration Test Volume
___ 1	Wholehouse	Proposed ACH(50)	0.00034	5595	306.95	576.27	0.1035	4.0	All	83924 cu ft

GARAGE

✓ #	Floor Area	Roof Area	Exposed Wall Perimeter	Avg. Wall Height	Exposed Wall Insulation
___ 1	862 ft²	862 ft²	96 ft	12 ft	1

MASS

✓ #	Mass Type	Area	Thickness	Furniture Fraction	Space
___ 1	Default(8 lbs/sq.ft.)	0 ft²	0 ft	0.30	SPACE 1
___ 2	Default(8 lbs/sq.ft.)	0 ft²	0 ft	0.30	SPACE 2
___ 3	Default(8 lbs/sq.ft.)	0 ft²	0 ft	0.30	SPACE 3

HEATING SYSTEM

✓ #	System Type	Subtype	AHRI #	Efficiency	Capacity kBtu/hr	----Geothermal HeatPump----				Ducts	Block
						Entry	Power	Volt	Current		
___ 1	Electric Strip Heat	None		COP: 1.00	34.1		0.00	0.00	0.00	sys#1	1
___ 2	Electric Strip Heat	None		COP: 1.00	34.1		0.00	0.00	0.00	sys#2	2
___ 3	Electric Strip Heat	None		COP: 1.00	23.9		0.00	0.00	0.00	sys#3	3

COOLING SYSTEM

✓ #	System Type	Subtype/Speed	AHRI #	Efficiency	Capacity kBtu/hr	Air Flow cfm	SHR	Duct	Block
___ 1	Central Unit	Split/Single		SEER2:15.2	55.5	1665	0.75	sys#1	1
___ 2	Central Unit	Split/Single		SEER2:15.2	55.5	1665	0.75	sys#2	2
___ 3	Central Unit	Split/Single		SEER2:15.2	34.2	1026	0.75	sys#3	3

HOT WATER SYSTEM

✓ #	System Type	Subtype	Location	EF(UEF)	Cap	Use	SetPnt	Fixture Flow	Pipe Ins.	Pipe length
___ 1	Propane	Tankless	SPACE 1	0.59 (0.59)	1.00 gal	90 gal	120 deg	Standard	=>R-3	30
	Recirculation System	Recirc Control Type	Loop length	Branch length	Pump power	DWHR	Facilities Connected	Equal Flow	DWHR Eff	Other Credits
___ 1	No		NA	NA	NA	No	NA	NA	NA	None

INPUT SUMMARY CHECKLIST REPORT

DUCTS

✓ Duct #	-----Supply-----			-----Return-----			Leakage Type	Air Handler	CFM 25 TOT	CFM 25 OUT	QN	RLF	HVAC #	
	Location	R-Value	Area	Location	R-Value	Area							Heat	Cool
___ 1 Attic		6.0	395 ft²	Attic	6.0	280 ft²	Default Leakage	SPACE 1	(Default)	(Default)			1	1
___ 2 Attic		6.0	305 ft²	SPACE 2	6.0	20 ft²	Default Leakage	SPACE 2	(Default)	(Default)			2	2
___ 3 Attic		6.0	160 ft²	SPACE 3	6.0	20 ft²	Default Leakage	SPACE 3	(Default)	(Default)			3	3

TEMPERATURES

Programable Thermostat: Y													
Ceiling Fans: N													
Cooling	☐ Jan	☐ Feb	☐ Mar	☐ Apr	☐ May	☒ Jun	☒ Jul	☒ Aug	☒ Sep	☐ Oct	☐ Nov	☐ Dec	
Heating	☒ Jan	☒ Feb	☒ Mar	☐ Apr	☐ May	☐ Jun	☐ Jul	☐ Aug	☐ Sep	☐ Oct	☒ Nov	☒ Dec	
Venting	☐ Jan	☐ Feb	☒ Mar	☒ Apr	☐ May	☐ Jun	☐ Jul	☐ Aug	☐ Sep	☒ Oct	☒ Nov	☐ Dec	
Thermostat Schedule: HERS 2006 Reference													
✓ Schedule Type		1	2	3	4	5	6	Hours 7	8	9	10	11	12
___ Cooling (WD)	AM PM	78 80	78 80	78 78	78 78	78 78	78 78	78 78	78 78	80 78	80 78	80 78	80 78
___ Cooling (WEH)	AM PM	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78
___ Heating (WD)	AM PM	66 68	66 68	66 68	66 68	66 68	68 68	68 68	68 68	68 68	68 68	68 66	68 66
___ Heating (WEH)	AM PM	66 68	66 68	66 68	66 68	66 68	68 68	68 68	68 68	68 68	68 68	68 66	68 66

ENERGY PERFORMANCE LEVEL (EPL) DISPLAY CARD

ESTIMATED ENERGY PERFORMANCE INDEX* = 99

The lower the EnergyPerformance Index, the more efficient the home.

7725 SOUTHWEST 114 STREET ,MIAMI,FL,33156

1. New construction or existing	New (From Plans)	10. Wall Types(6900.4 sqft.)	Insulation	Area
2. Single family or multiple family	Detached	a. Concrete Block - Int Insul, Exterior	R=5.0	6547.60 ft ²
3. Number of units, if multiple family	1	b. Frame - Steel, Adjacent	R=5.0	352.78 ft ²
4. Number of Bedrooms	6	c. N/A		
5. Is this a worst case?	No	d. N/A		
6. Conditioned floor area above grade (ft ²)	6331	11. Ceiling Types(6331.0 sqft.)	Insulation	Area
Conditioned floor area below grade (ft ²)	0	a. Flat ceiling under att (Vented)	R=30.0	3631.00 ft ²
7. Windows**	Description	b. Sloped ceiling under a (Vented)	R=30.0	2700.00 ft ²
a. U-Factor:	Sgl, U=1.05	c. N/A		
SHGC:	SHGC=0.31	12. Roof(Flat tile/slate, Vented)	Deck R=0.0	6673 ft ²
b. U-Factor:	N/A	13. Ducts, location & insulation level	R	ft ²
SHGC:		a. Sup: Attic, Ret: Attic, AH: SPACE 1	6	395
c. U-Factor:	N/A	b. Sup: Attic, Ret: SPACE 2, AH: SPACE 2	6	305
SHGC:		c. 1 additional duct system(s)	(see details)	
Area Weighted Average Overhang Depth:	4.633 ft	14. Cooling Systems	kBtu/hr	Efficiency
Area Weighted Average SHGC:	0.310	a. Central Unit	55.5	SEER2:15.20
8. Skylights	Description	b. Central Unit	55.5	SEER2:15.20
U-Factor:(AVG)	N/A	c. Central Unit	34.2	SEER2:15.20
SHGC(AVG):	N/A	15. Heating Systems	kBtu/hr	Efficiency
9. Floor Types	Insulation	a. Electric Strip Heat	34.1	COP:1.00
a. Slab-On-Grade Edge Insulation	R= 0.0	b. Electric Strip Heat	34.1	COP:1.00
b. N/A	R=	c. Electric Strip Heat	23.9	COP:1.00
c. N/A	R=	16. Hot Water Systems		
		a. PropaneTankless	Cap: 1 gallons	EF: 0.590
		b. Conservation features		
		17. Credits	None	Pstat

I certify that this home has complied with the Florida Energy Efficiency Code for Building Construction through the above energy saving features which will be installed (or exceeded) in this home before final inspection. Otherwise, a new EPL Display Card will be completed based on installed Code compliant features.

Builder Signature: _____ Date: _____

Address of New Home: 7725 SOUTHWEST 114 STREET City/FL Zip: MIAMI,FL,33156



*Note: This is not a Building Energy Rating. If your Index is below 70, your home may qualify for energy efficient mortgage (EEM) incentives if you obtain a Florida Energy Rating. For information about the Florida Building Code, Energy Conservation, contact the Florida Building Commission's support staff.

**Label required by Section R303.1.3 of the Florida Building Code, Energy Conservation, if not DEFAULT.

Florida Building Code, Energy Conservation, 7th Edition (2020)

Mandatory Requirements for Residential Performance, Prescriptive and ERI Methods

ADDRESS: 7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Permit Number:

MANDATORY REQUIREMENTS - See individual code sections for full details.

SECTION R401 GENERAL

- ☒ **R401.3 Energy Performance Level (EPL) display card - (Mandatory).** The building official shall require that an energy performance level (EPL) display card be completed and certified by the builder to be accurate and correct before final approval of the building for occupancy. Florida law (Section 553.9085, Florida Statutes) requires the EPL display card to be included as an addendum to each sales contract for both presold and nonpresold residential buildings. The EPL display card contains information indicating the energy performance level and efficiencies of components installed in a dwelling unit. The building official shall verify that the EPL display card completed and signed by the builder accurately reflects the plans and specifications submitted to demonstrate code compliance for the building. A copy of the EPL display card can be found in Appendix RD.

SECTION R402 BUILDING THERMAL ENVELOPE

- ☒ **R402.4 Air leakage (Mandatory).** The building thermal envelope shall be constructed to limit air leakage in accordance with the requirements of Sections R402.4.1 through R402.4.5.

Exception: Dwelling units of R-2 Occupancies and multiple attached single family dwellings shall be permitted to comply with Section C402.5.

- ☒ **R402.4.1 Building thermal envelope.** The building thermal envelope shall comply with Sections R402.4.1.1 and R402.4.1.2. The sealing methods between dissimilar materials shall allow for differential expansion and contraction.

- ☒ **R402.4.1.1 Installation.** The components of the building thermal envelope as listed in Table R402.4.1.1 shall be installed in accordance with the manufacturer's instructions and the criteria listed in Table R402.4.1.1, as applicable to the method of construction. Where required by the code official, an approved third party shall inspect all components and verify compliance.

- ☒ **R402.4.1.2 Testing.** The building or dwelling unit shall be tested and verified as having an air leakage rate not exceeding seven air changes per hour in Climate Zones 1 and 2, and three air changes per hour in Climate Zones 3 through 8. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.

Exception: Testing is not required for additions, alterations, renovations, or repairs, of the building thermal envelope of existing buildings in which the new construction is less than 85 percent of the building thermal envelope.

During testing:

1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures.
2. Dampers including exhaust, intake, makeup air, backdraft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures.
3. Interior doors, if installed at the time of the test, shall be open.
4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed.
5. Heating and cooling systems, if installed at the time of the test, shall be turned off.
6. Supply and return registers, if installed at the time of the test, shall be fully open.

- ☒ **R402.4.2 Fireplaces.** New wood-burning fireplaces shall have tight-fitting flue dampers or doors, and outdoor combustion air. Where using tight-fitting doors on factory-built fireplaces listed and labeled in accordance with UL 127, the doors shall be tested and listed for the fireplace. Where using tight-fitting doors on masonry fireplaces, the doors shall be listed and labeled in accordance with UL 907.

- ☒ **R402.4.3 Fenestration air leakage.** Windows, skylights and sliding glass doors shall have an air infiltration rate of no more than 0.3 cfm per square foot (1.5 L/s/m²), and swinging doors no more than 0.5 cfm per square foot (2.6 L/s/m²), when tested according to NFRC 400 or AAMA/WDMA/CSA 101/I.S.2/A440 by an accredited, independent laboratory and listed and labeled by the manufacturer.

Exception: Site-built windows, skylights and doors.

- ☒ **R402.4.4 Rooms containing fuel - burning appliances.** In Climate Zones 3 through 8, where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening shall be located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms shall be sealed and insulated in accordance with the envelope requirements of Table R402.1.2, where the walls, floors and ceilings shall meet not less than the basement wall R-value requirement. The door into the room shall be fully gasketed and any water lines and ducts in the room insulated in accordance with Section R403. The combustion air duct shall be insulated where it passes through conditioned space to a minimum of R-8.

Exceptions:

1. Direct vent appliances with both intake and exhaust pipes installed continuous to the outside.
2. Fireplaces and stoves complying with Section R402.4.2 and Section R1006 of the Florida Building Code, Residential.

MANDATORY REQUIREMENTS (Continued)

- ☒ **R402.4.5 Recessed lighting.** Recessed luminaires installed in the building thermal envelope shall be sealed to limit air leakage between conditioned and unconditioned spaces. All recessed luminaires shall be IC-rated and labeled as having an air leakage rate not more than 2.0 cfm (0.944 L/s) when tested in accordance with ASTM E283 at a 1.57 psf (75 Pa) pressure differential. All recessed luminaires shall be sealed with a gasket or caulk between the housing and the interior wall or ceiling covering.

SECTION R403 SYSTEMS

R403.1 Controls

☒ **R403.1.1 Thermostat provision (Mandatory).** At least one thermostat shall be provided for each separate heating and cooling system

☒ **R403.1.3 Heat pump supplementary heat (Mandatory).** Heat pumps having supplementary electric-resistance heat shall have controls that, except during defrost, prevent supplemental heat operation when the heat pump compressor can meet the heating load.

☒ **R403.3.2 Sealing (Mandatory).** All ducts, air handlers, filter boxes and building cavities that form the primary air containment passageways for air distribution systems shall be considered ducts or plenum chambers, shall be constructed and sealed in accordance with Section C403.2.9.2 of the Commercial Provisions of this code and shall be shown to meet duct tightness criteria below.

Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC 380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes, to be "substantially leak free" in accordance with Section R403.3.3.

☒ **R403.3.2.1 Sealed air handler.** Air handlers shall have a manufacturer's designation for an air leakage of no more than 2 percent of the design airflow rate when tested in accordance with ASHRAE 193.

☒ **R403.3.3 Duct testing (Mandatory).** Ducts shall be pressure tested to determine air leakage by one of the following methods:

1. Rough-in test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the system, including the manufacturer's air handler enclosure if installed at the time of the test. All registers shall be taped or otherwise sealed during the test.
2. Postconstruction test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the entire system, including the manufacturer's air handler enclosure. Registers shall be taped or otherwise sealed during the test.

Exceptions;

1. A duct air leakage test shall not be required where the ducts and air handlers are located entirely within the building thermal envelope.
2. Duct testing is not mandatory for buildings complying by Section 405 of this code. Duct leakage testing is required for Section R405 compliance where credit is taken for leakage, and a duct air leakage Q_n to the outside of less than 0.080 (where Q_n = duct leakage to the outside in cfm per 100 square feet of conditioned floor area tested at 25 Pascals) is indicated in the compliance report for the proposed design.

A written report of the results of the test shall be signed by the party conducting the test and provided to the code official

☒ **R403.3.5 Building cavities (Mandatory).** Building framing cavities shall not be used as ducts or plenums

☒ **R403.4 Mechanical system piping insulation (Mandatory).** Mechanical system piping capable of carrying fluids above 105°F (41°C) or below 55°F (13°C) shall be insulated to a minimum of R-3.

☒ **R403.4.1 Protection of piping insulation.** Piping insulation exposed to weather shall be protected from damage, including that caused by sunlight, moisture, equipment maintenance and wind, and shall provide shielding from solar radiation that can cause degradation of the material. Adhesive tape shall not be permitted.

☒ **R403.5.1 Heated water circulation and temperature maintenance systems (Mandatory).** If heated water circulation systems are installed, they shall be in accordance with Section R403.5.1.1. Heat trace temperature maintenance systems shall be in accordance with Section R403.5.1.2. Automatic controls, temperature sensors and pumps shall be accessible. Manual controls shall be readily accessible.

☒ **R403.5.1.1 Circulation systems.** Heated water circulation systems shall be provided with a circulation pump. The system return pipe shall be a dedicated return pipe or a cold water supply pipe. Gravity and thermosiphon circulation systems shall be prohibited. Controls for circulating hot water system pumps shall start the pump based on the identification of a demand for hot water within the occupancy. The controls shall automatically turn off the pump when the water in the circulation loop is at the desired temperature and when there is no demand for hot water.

☒ **R403.5.1.2 Heat trace systems.** Electric heat trace systems shall comply with IEEE 515.1 or UL 515. Controls for such systems shall automatically adjust the energy input to the heat tracing to maintain the desired water temperature in the piping in accordance with the times when heated water is used in the occupancy.

MANDATORY REQUIREMENTS (Continued)

☒ **R403.5.5 Heat traps (Mandatory).** Storage water heaters not equipped with integral heat traps and having vertical pipe risers shall have heat traps installed on both the inlets and outlets. External heat traps shall consist of either a commercially available heat trap or a downward and upward bend of at least 3 1/2 inches (89 mm) in the hot water distribution line and cold water line located as close as possible to the storage tank.

☒ **R403.5.6 Water heater efficiencies (Mandatory).**

R403.5.6.1.1 Automatic controls. Service water-heating systems shall be equipped with automatic temperature controls capable of adjustment from the lowest to the highest acceptable temperature settings for the intended use. The minimum temperature setting range shall be from 100°F to 140°F (38°C to 60°C).

R403.5.6.1.2 Shut down. A separate switch or a clearly marked circuit breaker shall be provided to permit the power supplied to electric service systems to be turned off. A separate valve shall be provided to permit the energy supplied to the main burner(s) of combustion types of service water-heating systems to be turned off.

☒ **R403.5.6.2 Water-heating equipment.** Water-heating equipment installed in residential units shall meet the minimum efficiencies of Table C404.2 in Chapter 4 of the Florida Building Code, Energy Conservation, Commercial Provisions, for the type of equipment installed. Equipment used to provide heating functions as part of a combination system shall satisfy all stated requirements for the appropriate water-heating category. Solar water heaters shall meet the criteria of Section R403.5.6.2.1.

☒ **R403.5.6.2.1 Solar water-heating systems.** Solar systems for domestic hot water production are rated by the annual solar energy factor of the system. The solar energy factor of a system shall be determined from the Florida Solar Energy Center Directory of Certified Solar Systems. Solar collectors shall be tested in accordance with ISO Standard 9806, Test Methods for Solar Collectors, and SRCC Standard TM-1, Solar Domestic Hot Water System and Component Test Protocol. Collectors in installed solar water-heating systems should meet the following criteria:

1. Be installed with a tilt angle between 10 degrees and 40 degrees of the horizontal; and
2. Be installed at an orientation within 45 degrees of true south.

☒ **R403.6 Mechanical ventilation (Mandatory).** The building shall be provided with ventilation that meets the requirements of the Florida Building Code, Residential, or Florida Building Code, Mechanical, as applicable, or with other approved means of ventilation including: Natural, Infiltration or Mechanical means. Outdoor air intakes and exhausts shall have automatic or gravity dampers that close when the ventilation system is not operating.

☒ **R403.6.1 Whole-house mechanical ventilation system fan efficacy.** When installed to function as a whole-house mechanical ventilation system, fans shall meet the efficacy requirements of Table R403.6.1.

Exception: Where an air handler that is integral to tested and listed HVAC equipment is used to provide whole-house mechanical ventilation, the air handler shall be powered by an electronically commutated motor.

☒ **R403.6.2 Ventilation Air.** Residential buildings designed to be operated at a positive indoor pressure or for mechanical ventilation shall meet the following criteria:

1. The design air change per hour minimums for residential buildings in ASHRAE 62.2, Ventilation for Acceptable Indoor Air Quality, shall be the maximum rates allowed for residential applications.
2. No ventilation or air-conditioning system make-up air shall be provided to conditioned space from attics, crawlspaces, attached enclosed garages or outdoor spaces adjacent to swimming pools or spas.
3. If ventilation air is drawn from enclosed space(s), then the walls of the space(s) from which air is drawn shall be insulated to a minimum of R-11 and the ceiling shall be insulated to a minimum of R-19, space permitting, or R-10 otherwise.

☒ **R403.7 Heating and cooling equipment.**

R403.7.1 Equipment sizing (Mandatory). Heating and cooling equipment shall be sized in accordance with ACCA Manual S based on the equipment loads calculated in accordance with ACCA Manual J or other approved heating and cooling calculation methodologies, based on building loads for the directional orientation of the building. The manufacturer and model number of the outdoor and indoor units (if split system) shall be submitted along with the sensible and total cooling capacities at the design conditions described in Section R302.1. This Code does not allow designer safety factors, provisions for future expansion or other factors that affect equipment sizing. System sizing calculations shall not include loads created by local intermittent mechanical ventilation such as standard kitchen and bathroom exhaust systems. New or replacement heating and cooling equipment shall have an efficiency rating equal to or greater than the minimum required by federal law for the geographic location where the equipment is installed.

MANDATORY REQUIREMENTS (Continued)

TABLE R403.6.1
WHOLE-HOUSE MECHANICAL VENTILATION SYSTEM FAN EFFICACY

FAN LOCATION	AIRFLOW RATE MINIMUM (CFM)	MINIMUM EFFICACY ^a (CFM/WATT)	AIRFLOW RATE MAXIMUM (CFM)
HRV or ERV	Any	1.2 cfm/watt	Any
Range hoods	Any	2.8 cfm/watt	Any
In-line fan	Any	2.8 cfm/watt	Any
Bathroom, utility room	10	1.4 cfm/watt	<90
Bathroom, utility room	90	2.8 cfm/watt	Any

For SI: 1 cfm = 28.3 L/min.

a. When tested in accordance with HVI Standard 916

☒ **R403.7.1.1 Cooling equipment capacity.** Cooling only equipment shall be selected so that its total capacity is not less than the calculated total load but not more than 1.15 times greater than the total load calculated according to the procedure selected in Section R403.7, or the closest available size provided by the manufacturer's product lines. The corresponding latent capacity of the equipment shall not be less than the calculated latent load.
The published value for AHRI total capacity is a nominal, rating-test value and shall not be used for equipment sizing. Manufacturer's expanded performance data shall be used to select cooling-only equipment. This selection shall be based on the outdoor design dry-bulb temperature for the load calculation (or entering water temperature for water-source equipment), the blower CFM provided by the expanded performance data, the design value for entering wet-bulb temperature and the design value for entering dry-bulb temperature.

Design values for entering wet-bulb and dry-bulb temperatures shall be for the indoor dry bulb and relative humidity used for the load calculation and shall be adjusted for return side gains if the return duct(s) is installed in an unconditioned space.

Exceptions:

1. Attached single- and multiple-family residential equipment sizing may be selected so that its cooling capacity is less than the calculated total sensible load but not less than 80 percent of that load.
2. When signed and sealed by a Florida-registered engineer, in attached single- and multiple-family units, the capacity of equipment may be sized in accordance with good design practice.

R403.7.1.2 Heating equipment capacity.

☒ **R403.7.1.2.1 Heat pumps.** Heat pump sizing shall be based on the cooling requirements as calculated according to Section R403.7.1.1, and the heat pump total cooling capacity shall not be more than 1.15 times greater than the design cooling load even if the design heating load is 1.15 times greater than the design cooling load.

☒ **R403.7.1.2.2 Electric resistance furnaces.** Electric resistance furnaces shall be sized within 4 kW of the design requirements calculated according to the procedure selected in Section R403.7.1.

☒ **R403.7.1.2.3 Fossil fuel heating equipment.** The capacity of fossil fuel heating equipment with natural draft atmospheric burners shall not be less than the design load calculated in accordance with Section R403.7.1.

☒ **R403.7.1.3 Extra capacity required for special occasions.** Residences requiring excess cooling or heating equipment capacity on an intermittent basis, such as anticipated additional loads caused by major entertainment events, shall have equipment sized or controlled to prevent continuous space cooling or heating within that space by one or more of the following options:

1. A separate cooling or heating system is utilized to provide cooling or heating to the major entertainment areas.
2. A variable capacity system sized for optimum performance during base load periods is utilized.

☒ **R403.8 Systems serving multiple dwelling units (Mandatory).** Systems serving multiple dwelling units shall comply with Sections C403 and C404 of the Florida Building Code, Energy Conservation—Commercial Provisions in lieu of Section R403.

☒ **R403.9 Snow melt and ice system controls (Mandatory).** Snow- and ice-melting systems, supplied through energy service to the building, shall include automatic controls capable of shutting off the system when the pavement temperature is above 50°F (10°C), and no precipitation is falling and an automatic or manual control that will allow shutoff when the outdoor temperature is above 40°F (4.8°C).

☒ **403.10 Pools and permanent spa energy consumption (Mandatory).** The energy consumption of pools and permanent spas shall be in accordance with Sections R403.10.1 through R403.10.5.

☒ **R403.10.1 Heaters.** The electric power to heaters shall be controlled by a readily accessible on-off switch that is an integral part of the heater mounted on the exterior of the heater, or external to and within 3 feet (914 mm) of the heater. Operation of such switch shall not change the setting of the heater thermostat. Such switches shall be in addition to a circuit breaker for the power to the heater.
Gas-fired heaters shall not be equipped with continuously burning ignition pilots.

MANDATORY REQUIREMENTS (Continued)

R403.10.2 Time switches. Time switches or other control methods that can automatically turn off and on according to a preset schedule shall be installed for heaters and pump motors. Heaters and pump motors that have built-in time switches shall be in compliance with this section.

Exceptions:

1. Where public health standards require 24-hour pump operation.
2. Pumps that operate solar- and waste-heat-recovery pool heating systems
3. Where pumps are powered exclusively from on-site renewable generation.

R403.10.3 Covers. Outdoor heated swimming pools and outdoor permanent spas shall be equipped with a vapor-retardant cover on or at the water surface or a liquid cover or other means proven to reduce heat loss.

Exception: Where more than 70 percent of the energy for heating, computed over an operation season, is from site-recovered energy, such as from a heat pump or solar energy source, covers or other vapor-retardant means shall not be required

R403.10.4 Gas- and oil-fired pool and spa heaters. All gas- and oil-fired pool and spa heaters shall have a minimum thermal efficiency of 82 percent for heaters manufactured on or after April 16, 2013, when tested in accordance with ANSI Z 21.56. Pool heaters fired by natural or LP gas shall not have continuously burning pilot lights.

R403.10.5 Heat pump pool heaters. Heat pump pool heaters shall have a minimum COP of 4.0 when tested in accordance with AHRI 1160, Table 2, Standard Rating Conditions-Low Air Temperature. A test report from an independent laboratory is required to verify procedure compliance. Geothermal swimming pool heat pumps are not required to meet this standard.

R403.11 Portable spas (Mandatory). The energy consumption of electric-powered portable spas shall be controlled by the requirements of APSP-14

R403.13 Dehumidifiers (Mandatory). If installed, a dehumidifier shall conform to the following requirements:

1. The minimum rated efficiency of the dehumidifier shall be greater than 1.7 liters/ kWh if the total dehumidifier capacity for the house is less than 75 pints/day and greater than 2.38 liters/kWh if the total dehumidifier capacity for the house is greater than or equal to 75 pints/day.
2. The dehumidifier shall be controlled by a sensor that is installed in a location where it is exposed to mixed house air.
3. Any dehumidifier unit located in unconditioned space that treats air from conditioned space shall be insulated to a minimum of R-2.
4. Condensate disposal shall be in accordance with Section M1411.3.1 of the Florida Building Code, Residential.

R403.13.1 Ducted dehumidifiers. Ducted dehumidifiers shall, in addition to conforming to the requirements of Section R403.13, conform to the following requirements:

1. If a ducted dehumidifier is configured with return and supply ducts both connected into the supply side of the cooling system, a backdraft damper shall be installed in the supply air duct between the dehumidifier inlet and outlet duct.
2. If a ducted dehumidifier is configured with only its supply duct connected into the supply side of the central heating and cooling system, a backdraft damper shall be installed in the dehumidifier supply duct between the dehumidifier and central supply duct.
3. A ducted dehumidifier shall not be ducted to or from a central ducted cooling system on the return duct side upstream from the central cooling evaporator coil.
4. Ductwork associated with a dehumidifier located in unconditioned space shall be insulated to a minimum of R-6.

SECTION R404 ELECTRICAL POWER AND LIGHTING SYSTEMS

R404.1 Lighting equipment (Mandatory). Not less than 90 percent of the lamps in permanently installed luminaires shall have an efficacy of at least 45 lumens-per-watt or shall utilize lamps with an efficacy of not less than 65 lumens-per-watt.

R404.1.1 Lighting equipment (Mandatory). uel gas lighting systems shall not have continuously burning pilot lights.

2020 - AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA
TABLE 402.4.1.1

AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA^a

Project Name: PINECREST RESIDENCE Street: 7725 SOUTHWEST 114 STREET City, State, Zip: MIAMI, FL, 33156 Owner: Design Location: FL, Miami		Builder Name: Permit Office: Permit Number: Jurisdiction: County: Miami-Dade(Florida Climate Zone 1)		CHECK
COMPONENT	AIR BARRIER CRITERIA	INSULATION INSTALLATION CRITERIA		
General requirements	A continuous air barrier shall be installed in the building envelope. The exterior thermal envelope contains a continuous air barrier. Breaks or joints in the air barrier shall be sealed.	Air-permeable insulation shall not be used as a sealing material.		✓
Ceiling/attic	The air barrier in any dropped ceiling/soffit shall be aligned with the insulation and any gaps in the air barrier shall be sealed. Access openings, drop down stairs or knee wall doors to unconditioned attic spaces shall be sealed.	The insulation in any dropped ceiling/soffit shall be aligned with the air barrier.		✓
Walls	The junction of the foundation and sill plate shall be sealed. The junction of the top plate and the top of exterior walls shall be sealed. Knee walls shall be sealed.	Cavities within corners and headers of frame walls shall be insulated by completely filling the cavity with a material having a thermal resistance of R-3 per inch minimum. Exterior thermal envelope insulation for framed walls shall be installed in substantial contact and continuous alignment with the air barrier.		✓
Windows, skylights and doors	The space between window/door jambs and framing, and skylights and framing shall be sealed.			✓
Rim joists	Rim joists shall include the air barrier.	Rim joists shall be insulated.		✓
Floors (including above-garage and cantilevered floors)	The air barrier shall be installed at any exposed edge of insulation.	Floor framing cavity insulation shall be installed to maintain permanent contact with the underside of subfloor decking, or floor framing cavity insulation shall be permitted to be in contact with the top side of sheathing, or continuous insulation installed on the underside of floor framing and extends from the bottom to the top of all perimeter floor framing members.		✓
Crawl space walls	Exposed earth in unvented crawl spaces shall be covered with a Class I vapor retarder with overlapping joints taped.	Where provided instead of floor insulation, insulation shall be permanently attached to the crawlspace walls.		N/A
Shafts, penetrations	Duct shafts, utility penetrations, and flue shafts opening to exterior or unconditioned space shall be sealed.			✓
Narrow cavities		Batts in narrow cavities shall be cut to fit, or narrow cavities shall be filled by insulation that on installation readily conforms to the available cavity spaces.		✓
Garage separation	Air sealing shall be provided between the garage and conditioned spaces.			✓
Recessed lighting	Recessed light fixtures installed in the building thermal envelope shall be sealed to the finished surface.	Recessed light fixtures installed in the building thermal envelope shall be air tight and IC rated.		✓
Plumbing and wiring		Batt insulation shall be cut neatly to fit around wiring and plumbing in exterior walls, or insulation that on installation readily conforms to available space shall extend behind piping and wiring.		✓
Shower/tub on exterior wall	The air barrier installed at exterior walls adjacent to showers and tubs shall separate them from the showers and tubs.	Exterior walls adjacent to showers and tubs shall be insulated.		✓
Electrical/phone box on exterior walls	The air barrier shall be installed behind electrical or communication boxes or air-sealed boxes shall be installed.			✓
HVAC register boots	HVAC supply and return register boots that penetrate building thermal envelope shall be sealed to the sub-floor, wall covering or ceiling penetrated by the boot.			✓
Concealed sprinklers	When required to be sealed, concealed fire sprinklers shall only be sealed in a manner that is recommended by the manufacturer. Caulking or other adhesive sealants shall not be used to fill voids between fire sprinkler cover plates and walls or ceilings.			N/A

a. In addition, inspection of log walls shall be in accordance with the provisions of ICC-400.

Envelope Leakage Test Report (Blower Door Test)

Residential Prescriptive, Performance or ERI Method Compliance

2020 Florida Building Code, Energy Conservation, 7th Edition

Jurisdiction:	Permit #:
Job Information	
Builder:	Community:
Lot: NA	
Address: 7725 SOUTHWEST 114 STREET	
City: MIAMI	State: FL
Zip: 33156	
Air Leakage Test Results <i>Passing results must meet either the Performance, Prescriptive, or ERI Method</i>	
☐ PRESCRIPTIVE METHOD-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding 7 air changes per hour at a pressure of 0.2 inch w.g. (50 Pascals) in Climate Zones 1 and 2. ☒ PERFORMANCE or ERI METHOD-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding the selected ACH(50) value, as shown on Form R405-2020 (Performance) or R406-2020 (ERI), section labeled as infiltration, sub-section ACH50. ACH(50) specified on Form R405-2020-Energy Calc (Performance) or R406-2020 (ERI): 4.000	
$\frac{\text{CFM}(50)}{\text{Building Volume}} \times 60 \div \frac{83924}{\text{ACH}(50)} =$ ☐ PASS ☐ When ACH(50) is less than 3, Mechanical Ventilation installation must be verified by building department. Method for calculating building volume: ☐ Retrieved from architectural plans ☒ Code software calculated ☐ Field measured and calculated	
R402.4.1.2 Testing. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 Pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), <i>Florida Statutes</i>, or individuals licensed as set forth in Section 489.105(3)(f), (g), or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the <i>code official</i>. Testing shall be performed at any time after creation of all penetrations of the <i>building thermal envelope</i>. During testing: 1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures. 2. Dampers including exhaust, intake, makeup air, back draft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures. 3. Interior doors, if installed at the time of the test, shall be open. 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed. 5. Heating and cooling systems, if installed at the time of the test, shall be turned off. 6. Supply and return registers, if installed at the time of the test, shall be fully open.	
Testing Company	
Company Name: _____ Phone: _____ I hereby verify that the above Air Leakage results are in accordance with the 2020 7th Edition Florida Building Code Energy Conservation requirements according to the compliance method selected above. Signature of Tester: _____ Date of Test: _____ Printed Name of Tester: _____ License/Certification #: _____ Issuing Authority: _____	

Residential System Sizing Calculation

Summary

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE


3/29/2023

Location for weather data: Miami, FL - Defaults: Latitude(26) Altitude(30 ft.) Temp Range(L)					
Humidity data: Interior RH (50%) Outdoor wet bulb (77F) Humidity difference(57gr.)					
Winter design temperature(MJ8 99%)	52	F	Summer design temperature(MJ8 99%)	91	F
Winter setpoint	70	F	Summer setpoint	75	F
Winter temperature difference	18	F	Summer temperature difference	16	F
Total heating load calculation	81686	Btuh	Total cooling load calculation	126263	Btuh
Submitted heating capacity	% of calc	Btuh	Submitted cooling capacity	% of calc	Btuh
Total (Electric Strip Heat)	112.8	92120	Sensible (SHR = 0.75)	104.5	108900
			Latent	164.4	36300
			Total	115.0	145200

WINTER CALCULATIONS

Winter Heating Load (for 6331 sqft)


Load component	Load
Window total 1936 sqft	36587 Btuh
Wall total 4903 sqft	11945 Btuh
Door total 62 sqft	511 Btuh
Ceiling total 6331 sqft	3629 Btuh
Floor total See detail report	15017 Btuh
Infiltration 232 cfm	4582 Btuh
Duct loss	9416 Btuh
Subtotal	81686 Btuh
Ventilation Ex:0 cfm; Sup:0 cfm	0 Btuh
TOTAL HEAT LOSS	81686 Btuh

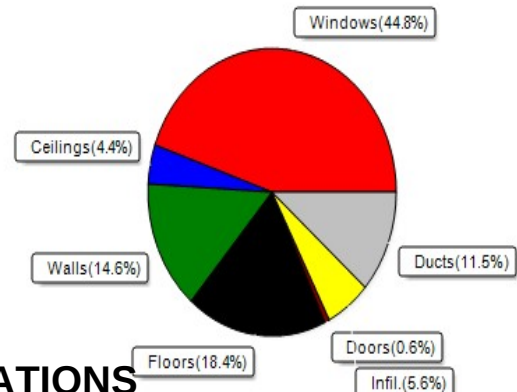

SUMMER CALCULATIONS

Summer Cooling Load (for 6331 sqft)

Load component	Load
Window total 1936 sqft	58667 Btuh
Wall total 4903 sqft	13192 Btuh
Door total 62 sqft	574 Btuh
Ceiling total 6331 sqft	6049 Btuh
Floor total	0 Btuh
Infiltration 174 cfm	3055 Btuh
Internal gain	14320 Btuh
Duct gain	8330 Btuh
Sens.Ventilation Ex:0 cfm; Sup:0 cfm	0 Btuh
Blower Load	0 Btuh
Total sensible gain	104186 Btuh
Latent gain(ducts)	3650 Btuh
Latent gain(infiltration)	6727 Btuh
Latent gain(ventilation)	0 Btuh
Latent gain(internal/occupants/other)	11700 Btuh
Total latent gain	22077 Btuh
TOTAL HEAT GAIN	126263 Btuh

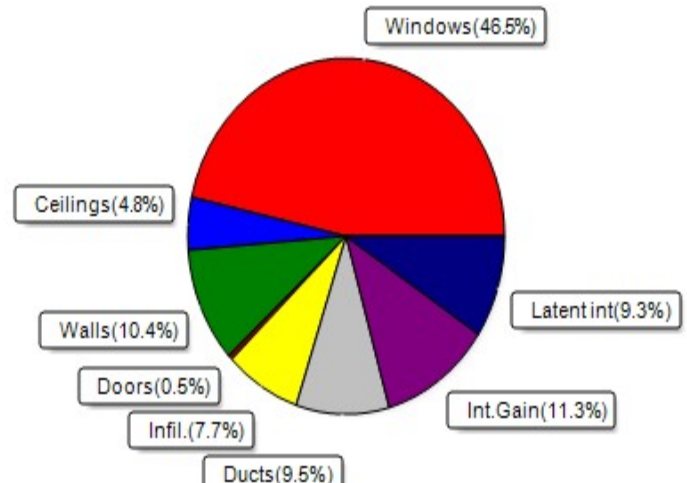

8th Edition

EnergyGauge® System Sizing

PREPARED BY: _____

DATE: _____

System Sizing Calculations - Winter

Residential Load - Room by Room Component Details

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE
Building Type: User

3/29/2023

Reference City: Miami, FL (Defaults) Winter Temperature Difference: 18.0 °F (MJ8 99%)
Winter Setpoint: 70 °F (Required Manual J default)

Component Loads for Room #1: SPACE 1

Window	Panes/Type	Frame	U	Orientation	Area(sqft)	X	HTM=	Load
2	1, NFRC 0.31	Metal	1.05	W	172.7		18.9	3263 Btuh
3	1, NFRC 0.31	Metal	1.05	W	18.0		18.9	340 Btuh
4	1, NFRC 0.31	Metal	1.05	S	12.0		18.9	227 Btuh
5	1, NFRC 0.31	Metal	1.05	S	35.0		18.9	662 Btuh
6	1, NFRC 0.31	Metal	1.05	E	43.2		18.9	816 Btuh
	Window Total				280.8(sqft)			5308 Btuh
Walls	Type	Ornt.	Ueff.	R-Value (Cav/Sh)	Area	X	HTM=	Load
1	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	846		2.37	2003 Btuh
2	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	149		2.37	352 Btuh
3	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	185		2.37	439 Btuh
4	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	131		2.37	311 Btuh
18	Frame - Steel - Adj		(0.184)	5.0/0.0	353		3.31	1169 Btuh
	Wall Total				1664(sqft)			4274 Btuh
Ceilings	Type/Color/Surface		Ueff.	R-Value	Area	X	HTM=	Load
1	Flat ceil/L/Tile		(0.032)	30.0/0.0	2191		0.57	1256 Btuh
	Ceiling Total				2191(sqft)			1256Btuh
Floors	Type		Ueff.	R-Value	Size	X	HTM=	Load
1	Slab On Grade		(1.180)	0.0	252.0 ft(perim.)		21.2	5352 Btuh
	Floor Total				2191 sqft			5352 Btuh
	Room Envelope Subtotal:							16190 Btuh
Infiltration	Type	Wholehouse	ACH	Room Volume	Wall Ratio	CFM=		
	Natural		0.17	23444	0.34	78.6		1555 Btuh
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Attic) (DLM of 0.251)							4456 Btuh
Room #1	Sensible Room Subtotal							22201 Btuh

Manual J Winter Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE
Building Type: User

3/29/2023

Component Loads for Room #2: SPACE 2

Window	Panes/Type	Frame	U	Orientation	Area(sqft)	X	HTM=	Load
1	1, NFRC 0.31	Metal	1.05	S	105.0		18.9	1984 Btuh
7	1, NFRC 0.31	Metal	1.05	S	147.5		18.9	2788 Btuh
8	1, NFRC 0.31	Metal	1.05	S	129.5		18.9	2447 Btuh
9	1, NFRC 0.31	Metal	1.05	S	27.0		18.9	510 Btuh
10	1, NFRC 0.31	Metal	1.05	W	54.0		18.9	1021 Btuh
11	1, NFRC 0.31	Metal	1.05	E	54.0		18.9	1021 Btuh
12	1, NFRC 0.31	Metal	1.05	E	95.3		18.9	1802 Btuh
13	1, NFRC 0.31	Metal	1.05	E	15.0		18.9	284 Btuh
14	1, NFRC 0.31	Metal	1.05	E	80.0		18.9	1512 Btuh
15	1, NFRC 0.31	Metal	1.05	N	200.0		18.9	3780 Btuh
16	1, NFRC 0.31	Metal	1.05	N	160.0		18.9	3024 Btuh
Window Total					1067.3(sqft)			20172 Btuh
Walls	Type	Ornt.	Ueff.	R-Value (Cav/Sh)	Area	X	HTM=	Load
5	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	246		2.37	583 Btuh
6	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	210		2.37	498 Btuh
7	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	221		2.37	523 Btuh
8	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	221		2.37	523 Btuh
9	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	65		2.37	153 Btuh
10	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	249		2.37	590 Btuh
11	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	304		2.37	721 Btuh
12	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	237		2.37	562 Btuh
Wall Total					1754(sqft)			4153 Btuh
Doors	Type	Storm	Ueff.		Area	X	HTM=	Load
1	Wood - Exterior,		w (0.460)		62		8.3	511 Btuh
Door Total					62(sqft)			511Btuh
Ceilings	Type/Color/Surface		Ueff.	R-Value	Area	X	HTM=	Load
2	Sloped ce/L/Tile		(0.032)	30.0/0.0	2700		0.57	1548 Btuh
Ceiling Total					2700(sqft)			1548Btuh
Floors	Type		Ueff.	R-Value	Size	X	HTM=	Load
2	Slab On Grade		(1.180)	0.0	262.0 ft(perim.)		21.2	5565 Btuh
Floor Total					2700 sqft			5565 Btuh
Room Envelope Subtotal:								31948 Btuh
Infiltration	Type	Wholehouse	ACH	Room Volume	Wall Ratio	CFM=		Load
	Natural		0.17	43200	0.36	82.8		1639 Btuh
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Cond.) (DLM of 0.098)							3291 Btuh

Manual J Winter Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE
Building Type: User

3/29/2023

Room #2	Sensible Room Subtotal	36878 Btuh
----------------	-------------------------------	-------------------

Component Loads for Room #3: SPACE 3

Window	Panes/Type	Frame	U	Orientation	Area(sqft)	X	HTM=	Load
17	1, NFRC 0.31	Metal	1.05	W	121.7		18.9	2300 Btuh
18	1, NFRC 0.31	Metal	1.05	W	12.0		18.9	227 Btuh
19	1, NFRC 0.31	Metal	1.05	W	80.0		18.9	1512 Btuh
20	1, NFRC 0.31	Metal	1.05	N	160.0		18.9	3024 Btuh
21	1, NFRC 0.31	Metal	1.05	E	18.0		18.9	340 Btuh
22	1, NFRC 0.31	Metal	1.05	E	12.0		18.9	227 Btuh
23	1, NFRC 0.31	Metal	1.05	E	24.0		18.9	454 Btuh
24	1, NFRC 0.31	Metal	1.05	S	160.0		18.9	3024 Btuh
	Window Total				587.7(sqft)			11107 Btuh
Walls	Type	Ornt.	Ueff.	R-Value (Cav/Sh)	Area	X	HTM=	Load
13	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	28		2.37	67 Btuh
14	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	337		2.37	798 Btuh
15	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	74		2.37	175 Btuh
16	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	972		2.37	2302 Btuh
17	Conc Blk,Hollow - Ext		(0.132)	5.0/0.0	74		2.37	175 Btuh
	Wall Total				1485(sqft)			3517 Btuh
Ceilings	Type/Color/Surface		Ueff.	R-Value	Area	X	HTM=	Load
3	Flat ceil/L/Tile		(0.032)	30.0/0.0	1440		0.57	825 Btuh
	Ceiling Total				1440(sqft)			825Btuh
Floors	Type		Ueff.	R-Value	Size	X	HTM=	Load
3	Slab On Grade		(1.180)	0.0	193.0 ft(perim.)		21.2	4099 Btuh
	Floor Total				1440 sqft			4099 Btuh
	Room Envelope Subtotal:							19549 Btuh
Infiltration	Type	Wholehouse	ACH	Room Volume	Wall Ratio	CFM=		
	Natural		0.17	17280	0.30	70.2		1388 Btuh
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Cond.) (DLM of 0.080)							1670 Btuh
Room #3	Sensible Room Subtotal							22607 Btuh

Manual J Winter Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE
Building Type: User

3/29/2023

SYSTEM GROUPS (BLOCK LOADS)

Heating Loads For System(s):1 Block #1:Block1 Serving Rooms: 1	Block load	22201 Btuh
---	------------	------------

Heating Loads For System(s):2 Block #2:Block2 Serving Rooms: 2	Block load	36878 Btuh
---	------------	------------

Heating Loads For System(s):3 Block #3:Block3 Serving Rooms: 3	Block load	22607 Btuh
---	------------	------------

WHOLE HOUSE TOTALS

Totals for Heating	Subtotal Sensible Heat Loss Ventilation Sens. Heat Loss (Ex:0 cfm; Sup:0 cfm) Total Heat Loss	81686 Btuh 0 Btuh 81686 Btuh
---------------------------	---	------------------------------------

EQUIPMENT

1. Electric Strip Heat		34120 Btuh
2. Electric Strip Heat		34120 Btuh
3. Electric Strip Heat		23880 Btuh

Manual J Winter Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE
Building Type: User

3/29/2023

Key: Window types - NFRC (Requires U-Factor and Shading coefficient(SHGC) of glass as numerical values)
or - Glass as 'Clear' or 'Tint' (Uses U-Factor and SHGC defaults)
U - (Window U-Factor)
HTM - (ManualJ Heat Transfer Multiplier)



Version 8

System Sizing Calculations - Summer

Residential Load - Room by Room Component Details

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

3/29/2023

Reference City: Miami, FL (Defaults)
Humidity difference: 57gr.

Temperature Difference: 16.0F(MJ8 99%)
Summer Setpoint: 75 °F (Required Manual J default)

Component Loads for Room #1: SPACE 1

Window	Type*						Overhang		Window Area(sqft)			HTM		Load
	Panes	SHGC	U	InSh	IS	Ornt	Len	Hgt	Gross	Shaded	Unshaded	Shaded	Unshaded	
2	1 NFRC	0.31,	1.05	No	No	W	3.0ft	1.0ft	172.7	36.8	135.9	24	47	7254 Btuh
3	1 NFRC	0.31,	1.05	No	No	W	3.0ft	1.0ft	18.0	4.5	13.5	24	47	741 Btuh
4	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	12.0	12.0	0.0	24	25	282 Btuh
5	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	35.0	35.0	0.0	24	25	823 Btuh
6	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	43.2	9.2	34.0	24	47	1813 Btuh
	Window Total								281 (sqft)					10913 Btuh
Walls	Type						U-Value	R-Value	Area(sqft)		HTM		Load	
								Cav/Sheath						
	1	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	845.6		2.7		2258 Btuh	
	2	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	148.8		2.7		397 Btuh	
	3	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	185.2		2.7		495 Btuh	
	4	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	131.5		2.7		351 Btuh	
	18	Frame - Steel - Adj					0.18	5.0/0.0	352.8		2.9		1039 Btuh	
	Wall Total								1664 (sqft)				4541 Btuh	
Ceilings	Type/Color/Surface						U-Value	R-Value	Area(sqft)		HTM		Load	
1	Vented Attic/Light/Tile					0.032	30.0/0.0	2191.0		0.96		2093 Btuh		
	Ceiling Total								2191 (sqft)				2093 Btuh	
Floors	Type						R-Value		Size		HTM		Load	
1	Slab On Grade					0.0		2191 (ft-perimeter)		0.0		0 Btuh		
	Floor Total								2191.0 (sqft)				0 Btuh	
	Zone Envelope Subtotal:													17548 Btuh
Infiltration	Type	Wholehouse ACH					Volume(cuft)		Wall Ratio		CFM=		Load	
	Natural	0.12					23444		0.34		59.0		1037 Btuh	
Internal gain	Occupants						Btuh/occupant		Appliance		Load			
	5						X	230	+	9400	10550 Btuh			
	Sensible Envelope Load:													29134 Btuh
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Attic)											(DGM of 0.168)		4904 Btuh
	Sensible Zone Load													34038 Btuh

Manual J Summer Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAMI_INTL_AP

3/29/2023

Component Loads for Room #2: SPACE 2

Window	Type*						Overhang		Window Area(sqft)			HTM		Load		
	Panes	SHGC	U	InSh	IS	Ornt	Len	Hgt	Gross	Shaded	Unshaded	Shaded	Unshaded			
1	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	105.0	105.0	0.0	24	25	2469	Btuh	
7	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	147.5	147.5	0.0	24	25	3468	Btuh	
8	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	129.5	129.5	0.0	24	25	3044	Btuh	
9	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	27.0	27.0	0.0	24	25	635	Btuh	
10	1 NFRC	0.31,	1.05	No	No	W	3.0ft	1.0ft	54.0	20.1	33.9	24	47	2066	Btuh	
11	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	54.0	20.1	33.9	24	47	2066	Btuh	
12	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	95.3	19.4	76.0	24	47	4027	Btuh	
13	1 NFRC	0.31,	1.05	No	No	E	6.0ft	1.0ft	15.0	11.9	3.1	24	47	425	Btuh	
14	1 NFRC	0.31,	1.05	No	No	E	6.0ft	1.0ft	80.0	31.8	48.2	24	47	3013	Btuh	
15	1 NFRC	0.31,	1.05	No	No	N	8.0ft	1.0ft	200.0	0.0	200.0	24	24	4703	Btuh	
16	1 NFRC	0.31,	1.05	No	No	N	8.0ft	1.0ft	160.0	0.0	160.0	24	24	3762	Btuh	
	Window Total								1067 (sqft)					29676 Btuh		
Walls	Type						U-Value	R-Value	Area(sqft)			HTM		Load		
								Cav/Sheath								
	5	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	246.4			2.7		658 Btuh		
	6	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	210.1			2.7		561 Btuh		
	7	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	221.0			2.7		590 Btuh		
	8	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	221.0			2.7		590 Btuh		
	9	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	64.7			2.7		173 Btuh		
	10	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	249.0			2.7		665 Btuh		
	11	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	304.4			2.7		813 Btuh		
	12	Concrete Blk,Hollow - Ext					0.13	5.0/0.0	237.1			2.7		633 Btuh		
		Wall Total								1754 (sqft)					4684 Btuh	
	Doors	Type								Area (sqft)			HTM		Load	
		1	Wood - Exterior							61.7			9.3		574 Btuh	
		Door Total								62 (sqft)					574 Btuh	
Ceilings	Type/Color/Surface						U-Value	R-Value	Area(sqft)			HTM		Load		
	2	Vented Attic/Light/Tile					0.032	30.0/0.0	2700.0			0.96		2580 Btuh		
		Ceiling Total								2700 (sqft)					2580 Btuh	
Floors	Type							R-Value	Size			HTM		Load		
	2	Slab On Grade						0.0	2700 (ft-perimeter)			0.0		0 Btuh		
		Floor Total								2700.0 (sqft)					0 Btuh	
	Zone Envelope Subtotal:													37513 Btuh		
Infiltration	Type						Wholehouse ACH		Volume(cuft)		Wall Ratio		CFM=		Load	
	Natural						0.12		43200		0.36		62.1		1093 Btuh	
Internal gain							Occupants		Btuh/occupant		Appliance		Load			
							0		X 230		+		2830		2830 Btuh	
	Sensible Envelope Load:													41436 Btuh		
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Cond.) (DGM of 0.054)													2241 Btuh		
	Sensible Zone Load													43676 Btuh		

Manual J Summer Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAAMI_INTL_AP

3/29/2023

Component Loads for Room #3: SPACE 3

Window	Type*						Overhang		Window Area(sqft)			HTM		Load
	Panes	SHGC	U	InSh	IS	Ornt	Len	Hgt	Gross	Shaded	Unshaded	Shaded	Unshaded	
17	1 NFRC	0.31,	1.05	No	No	W	3.0ft	1.0ft	121.7	18.1	103.5	24	47	5294 Btuh
18	1 NFRC	0.31,	1.05	No	No	W	6.0ft	1.0ft	12.0	12.0	0.0	24	47	282 Btuh
19	1 NFRC	0.31,	1.05	No	No	W	6.0ft	1.0ft	80.0	31.8	48.2	24	47	3013 Btuh
20	1 NFRC	0.31,	1.05	No	No	N	8.0ft	1.0ft	160.0	0.0	160.0	24	24	3762 Btuh
21	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	18.0	13.4	4.6	24	47	531 Btuh
22	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	12.0	8.9	3.1	24	47	354 Btuh
23	1 NFRC	0.31,	1.05	No	No	E	3.0ft	1.0ft	24.0	4.5	19.5	24	47	1023 Btuh
24	1 NFRC	0.31,	1.05	No	No	S	3.0ft	1.0ft	160.0	160.0	0.0	24	25	3762 Btuh
	Window Total								588 (sqft)					18021 Btuh
Walls	Type						U-Value	R-Value	Area(sqft)		HTM		Load	
							Cav/Sheath							
13	Concrete Blk,Hollow - Ext						0.13	5.0/0.0	28.3		2.7		76 Btuh	
14	Concrete Blk,Hollow - Ext						0.13	5.0/0.0	337.0		2.7		900 Btuh	
15	Concrete Blk,Hollow - Ext						0.13	5.0/0.0	74.0		2.7		198 Btuh	
16	Concrete Blk,Hollow - Ext						0.13	5.0/0.0	972.0		2.7		2596 Btuh	
17	Concrete Blk,Hollow - Ext						0.13	5.0/0.0	74.0		2.7		198 Btuh	
	Wall Total								1485 (sqft)					3967 Btuh
Ceilings	Type/Color/Surface						U-Value	R-Value	Area(sqft)		HTM		Load	
3	Vented Attic/Light/Tile						0.032	30.0/0.0	1440.0		0.96		1376 Btuh	
	Ceiling Total								1440 (sqft)					1376 Btuh
Floors	Type						R-Value		Size		HTM		Load	
3	Slab On Grade						0.0		1440 (ft-perimeter)		0.0		0 Btuh	
	Floor Total								1440.0 (sqft)					0 Btuh
	Zone Envelope Subtotal:												23364 Btuh	
Infiltration	Type	Wholehouse ACH					Volume(cuft)		Wall Ratio		CFM=		Load	
	Natural	0.12					17280		0.30		52.6		925 Btuh	
Internal gain	Occupants						Btuh/occupant		Appliance		Load			
	3						X 230		+		250		940 Btuh	
	Sensible Envelope Load:												25229 Btuh	
Duct load	Average sealed, Supply(R6.0-Attic), Return(R6.0-Cond.) (DGM of 0.047)											1183 Btuh		
	Sensible Zone Load												26412 Btuh	

Manual J Summer Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAMI_INTL_AP

3/29/2023

The following window Excursion will be assigned to the system loads.

Windows	July excursion for System 1	0 Btuh
	July excursion for System 2	0 Btuh
	July excursion for System 3	56 Btuh
	Excursion Subtotal:	56 Btuh
Duct load		3 Btuh
	Sensible Excursion Load	59 Btuh

Manual J Summer Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAMI_INTL_AP

3/29/2023

SYSTEM GROUPS (BLOCK LOADS)

Cooling Loads For System(s): 1 Block #1:Block1 Serving Zones: 1	Sensible Envelope Load	29134 Btuh
	Window Excursion	0 Btuh
	Sensible Duct Load (duct gain multiplier of 0.168)	4904 Btuh
	Sensible ventilation (Ex:0 cfm; Sup:0 cfm)	0 Btuh
	Zone Sensible gain	34038 Btuh
	Latent infiltration/ventilation gain	2283 Btuh
	Latent duct gain	2603 Btuh
	Latent occupant gain	1000 Btuh
	Latent other gain	8350 Btuh
	Total block load	48274 Btuh

Cooling Loads For System(s): 2 Block #2:Block2 Serving Zones: 2	Sensible Envelope Load	41436 Btuh
	Window Excursion	0 Btuh
	Sensible Duct Load (duct gain multiplier of 0.054)	2241 Btuh
	Sensible ventilation (Ex:0 cfm; Sup:0 cfm)	0 Btuh
	Zone Sensible gain	43676 Btuh
	Latent infiltration/ventilation gain	2406 Btuh
	Latent duct gain	676 Btuh
	Latent occupant gain	0 Btuh
	Latent other gain	1500 Btuh
	Total block load	48258 Btuh

Manual J Summer Calculations

Residential Load - Component Details (continued)

7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAMI_INTL_AP

3/29/2023

SYSTEM GROUPS (BLOCK LOADS)

Cooling Loads For System(s): 3 Block #3:Block3 Serving Zones: 3	Sensible Envelope Load	25229 Btuh
	Window Excursion	56 Btuh
	Sensible Duct Load (duct gain multiplier of 0.047) (Includes 3 Btuh due to window excursion)	1185 Btuh
	Sensible ventilation (Ex:0 cfm; Sup:0 cfm)	0 Btuh
	Zone Sensible gain	26471 Btuh
	Latent infiltration/ventilation gain	2038 Btuh
	Latent duct gain	372 Btuh
	Latent occupant gain	600 Btuh
	Latent other gain	250 Btuh
	Total block load	29730 Btuh

WHOLE HOUSE TOTALS

Whole House Totals for Cooling	Sensible Envelope Load All Zones	95855 Btuh
	Sensible Duct Load	8330 Btuh
	Total Sensible Zone Loads	104186 Btuh
	Sensible ventilation (Ex:0 cfm; Sup:0 cfm)	0 Btuh
	Blower	0 Btuh
	Total sensible gain	104186 Btuh
	Latent infiltration gain (for 57 gr. humidity difference)	6727 Btuh
	Latent ventilation gain	0 Btuh
	Latent duct gain	3650 Btuh
	Latent occupant gain (8.0 people @ 200 Btuh per person)	1600 Btuh
	Latent other gain	10100 Btuh
	Latent total gain	22077 Btuh
	TOTAL GAIN	126263 Btuh

EQUIPMENT

1. Central Unit	#	55500 Btuh
2. Central Unit	#	55500 Btuh
3. Central Unit	#	34200 Btuh

Manual J Summer Calculations

Residential Load - Component Details (continued)


7725 SOUTHWEST 114 STREET
MIAMI, FL 33156

Project Title:
PINECREST RESIDENCE

Climate:FL_MIAMI_INTL_AP

3/29/2023

*Key: Window types (Panels - Number and type of panes of glass)
(SHGC - Shading coefficient of glass as SHGC numerical value)
(U - Window U-Factor)
(InSh - Interior shading device: none(No), Blinds(B), Draperies(D) or Roller Shades(R))
- For Blinds: Assume medium color, half closed
For Draperies: Assume medium weave, half closed
For Roller shades: Assume translucent, half closed
(IS - Insect screen: none(N), Full(F) or Half($\frac{1}{2}$))
(Ornt - compass orientation)



Version 8
